



RANCHO CUCAMONGA FIRE PROTECTION DISTRICT


FIRE STATION NO. 178

CITY OF RANCHO CUCAMONGA



Activity ID	Activity Name	Duration	Start	Finish	2021												2022												2023												2024
					Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan		

RANCHO CUCAMONGA FIRE PROTECTION DISTRICT - RFP R1				
Administrative / Summary				
ADMN-100	Statement of Qualifications Due	1	17-Mar-21	17-Mar-21
ADMN-110	Issue RFP to Short List	1	01-Apr-21	01-Apr-21
ADMN-120	Proposal / Bid Due Date	1	15-Jun-21	15-Jun-21
ADMN-130	Selection and Notification	1	14-Jul-21	14-Jul-21
ADMN-140	Notice to Proceed	0	25-Jul-21	
ADMN-150	Project Duration in Calendar Days	557	25-Jul-21	01-Feb-23
ADMN-160	Project Completion (2/1/23)	0		01-Feb-23
Fire Station NO. 178				
Design				
DES-200	Kick of Meeting (Within 7 days of NTP)	1	30-Jul-21	30-Jul-21
DES-210	75% Design Development	30	30-Jul-21	28-Aug-21
DES-220	City Review / RCFPD of 75% DD	15	29-Aug-21	12-Sep-21
DES-230	100% Design Development	30	03-Sep-21	02-Oct-21
DES-240	City Review / RCFPD of 100% DD	15	03-Oct-21	17-Oct-21
DES-250	50% Construction Documents	30	08-Oct-21	06-Nov-21
DES-260	City Review / RCFPD of 50% CD	15	07-Nov-21	21-Nov-21
DES-270	100% Construction Documents	30	12-Nov-21	11-Dec-21
DES-280	City Review / RCFPD of 100% CD	46	12-Dec-21	26-Jan-22
DES-290	Permitting	40	27-Jan-22	07-Mar-22
DES-300	Back Check	10	08-Mar-22	17-Mar-22
DES-310	Construction Drawing Approvals	5	18-Mar-22	22-Mar-22
Construction				
CNST-400	Mobilization	2	07-Mar-22	09-Mar-22
CNST-410	Temporary Facilities	5	09-Mar-22	16-Mar-22
CNST-420	Soft Demolition	2	16-Mar-22	18-Mar-22
CNST-430	Hard Demolition	2	18-Mar-22	22-Mar-22
CNST-440	Import for Town Center Access	3	22-Mar-22	25-Mar-22
CNST-450	Earthwork	10	25-Mar-22	08-Apr-22
CNST-460	Site Utility	15	25-Mar-22	15-Apr-22

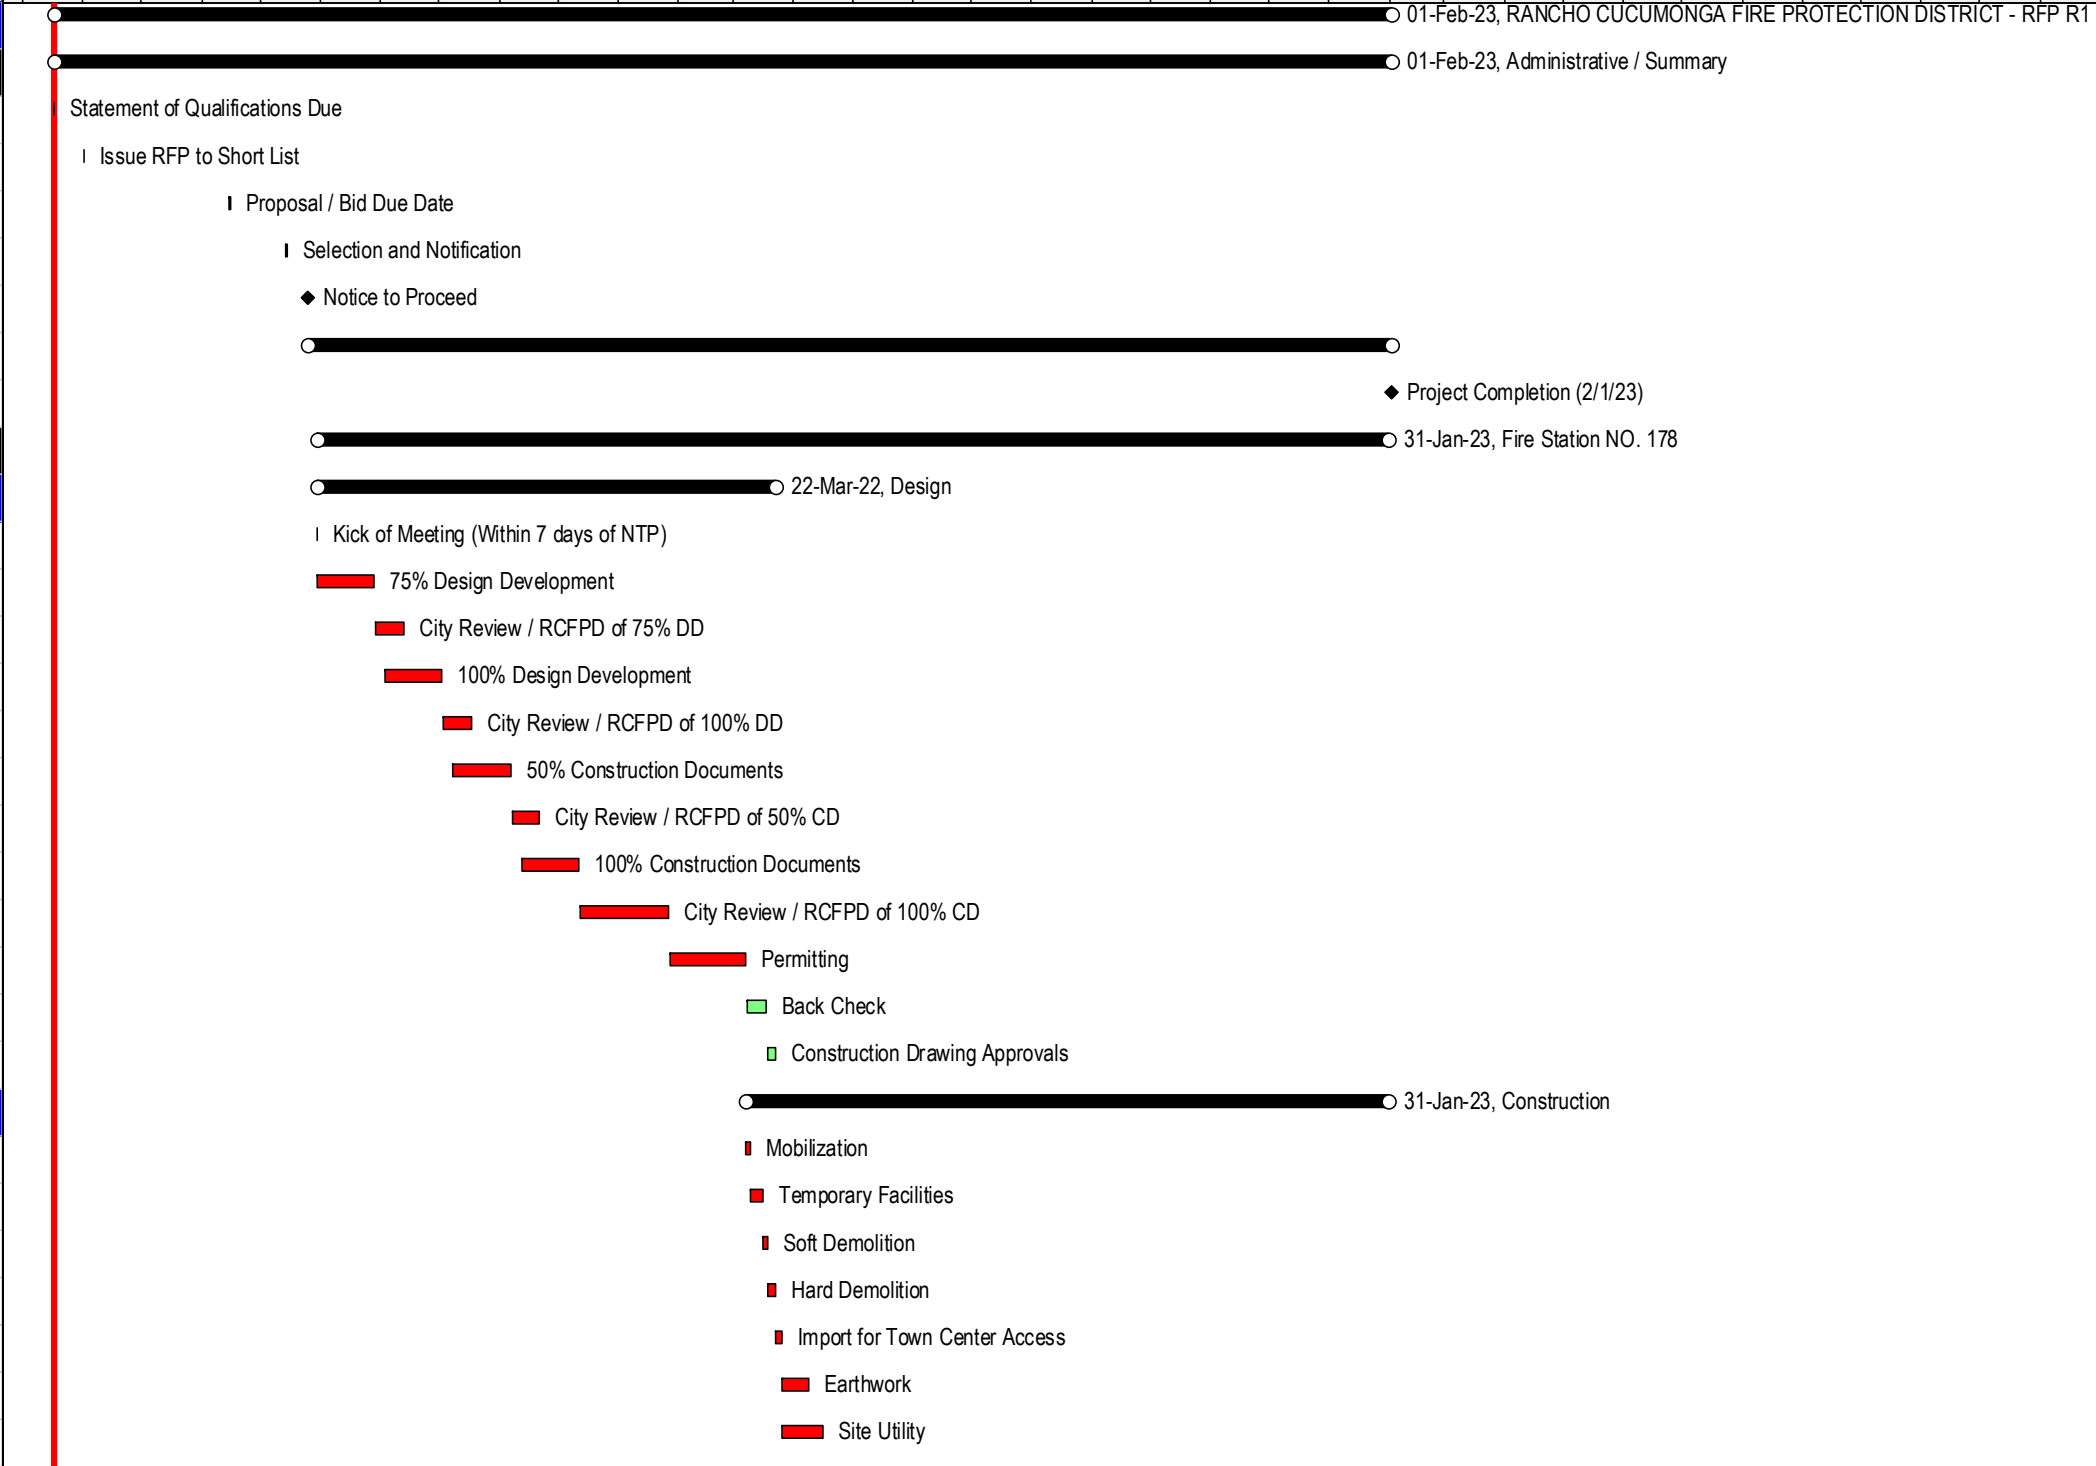

Remaining Level of Effort Summary
Remaining Work
Critical Work
Milestone

BID SCHEDULE

