




- Remaining Level of Effort
- Remaining Work
- Critical Work
- ◆ Milestone
- Summary

CONSTRUCTION SCHEDULE - OCT 2024
SUBCONTRACTORS - REMAINING

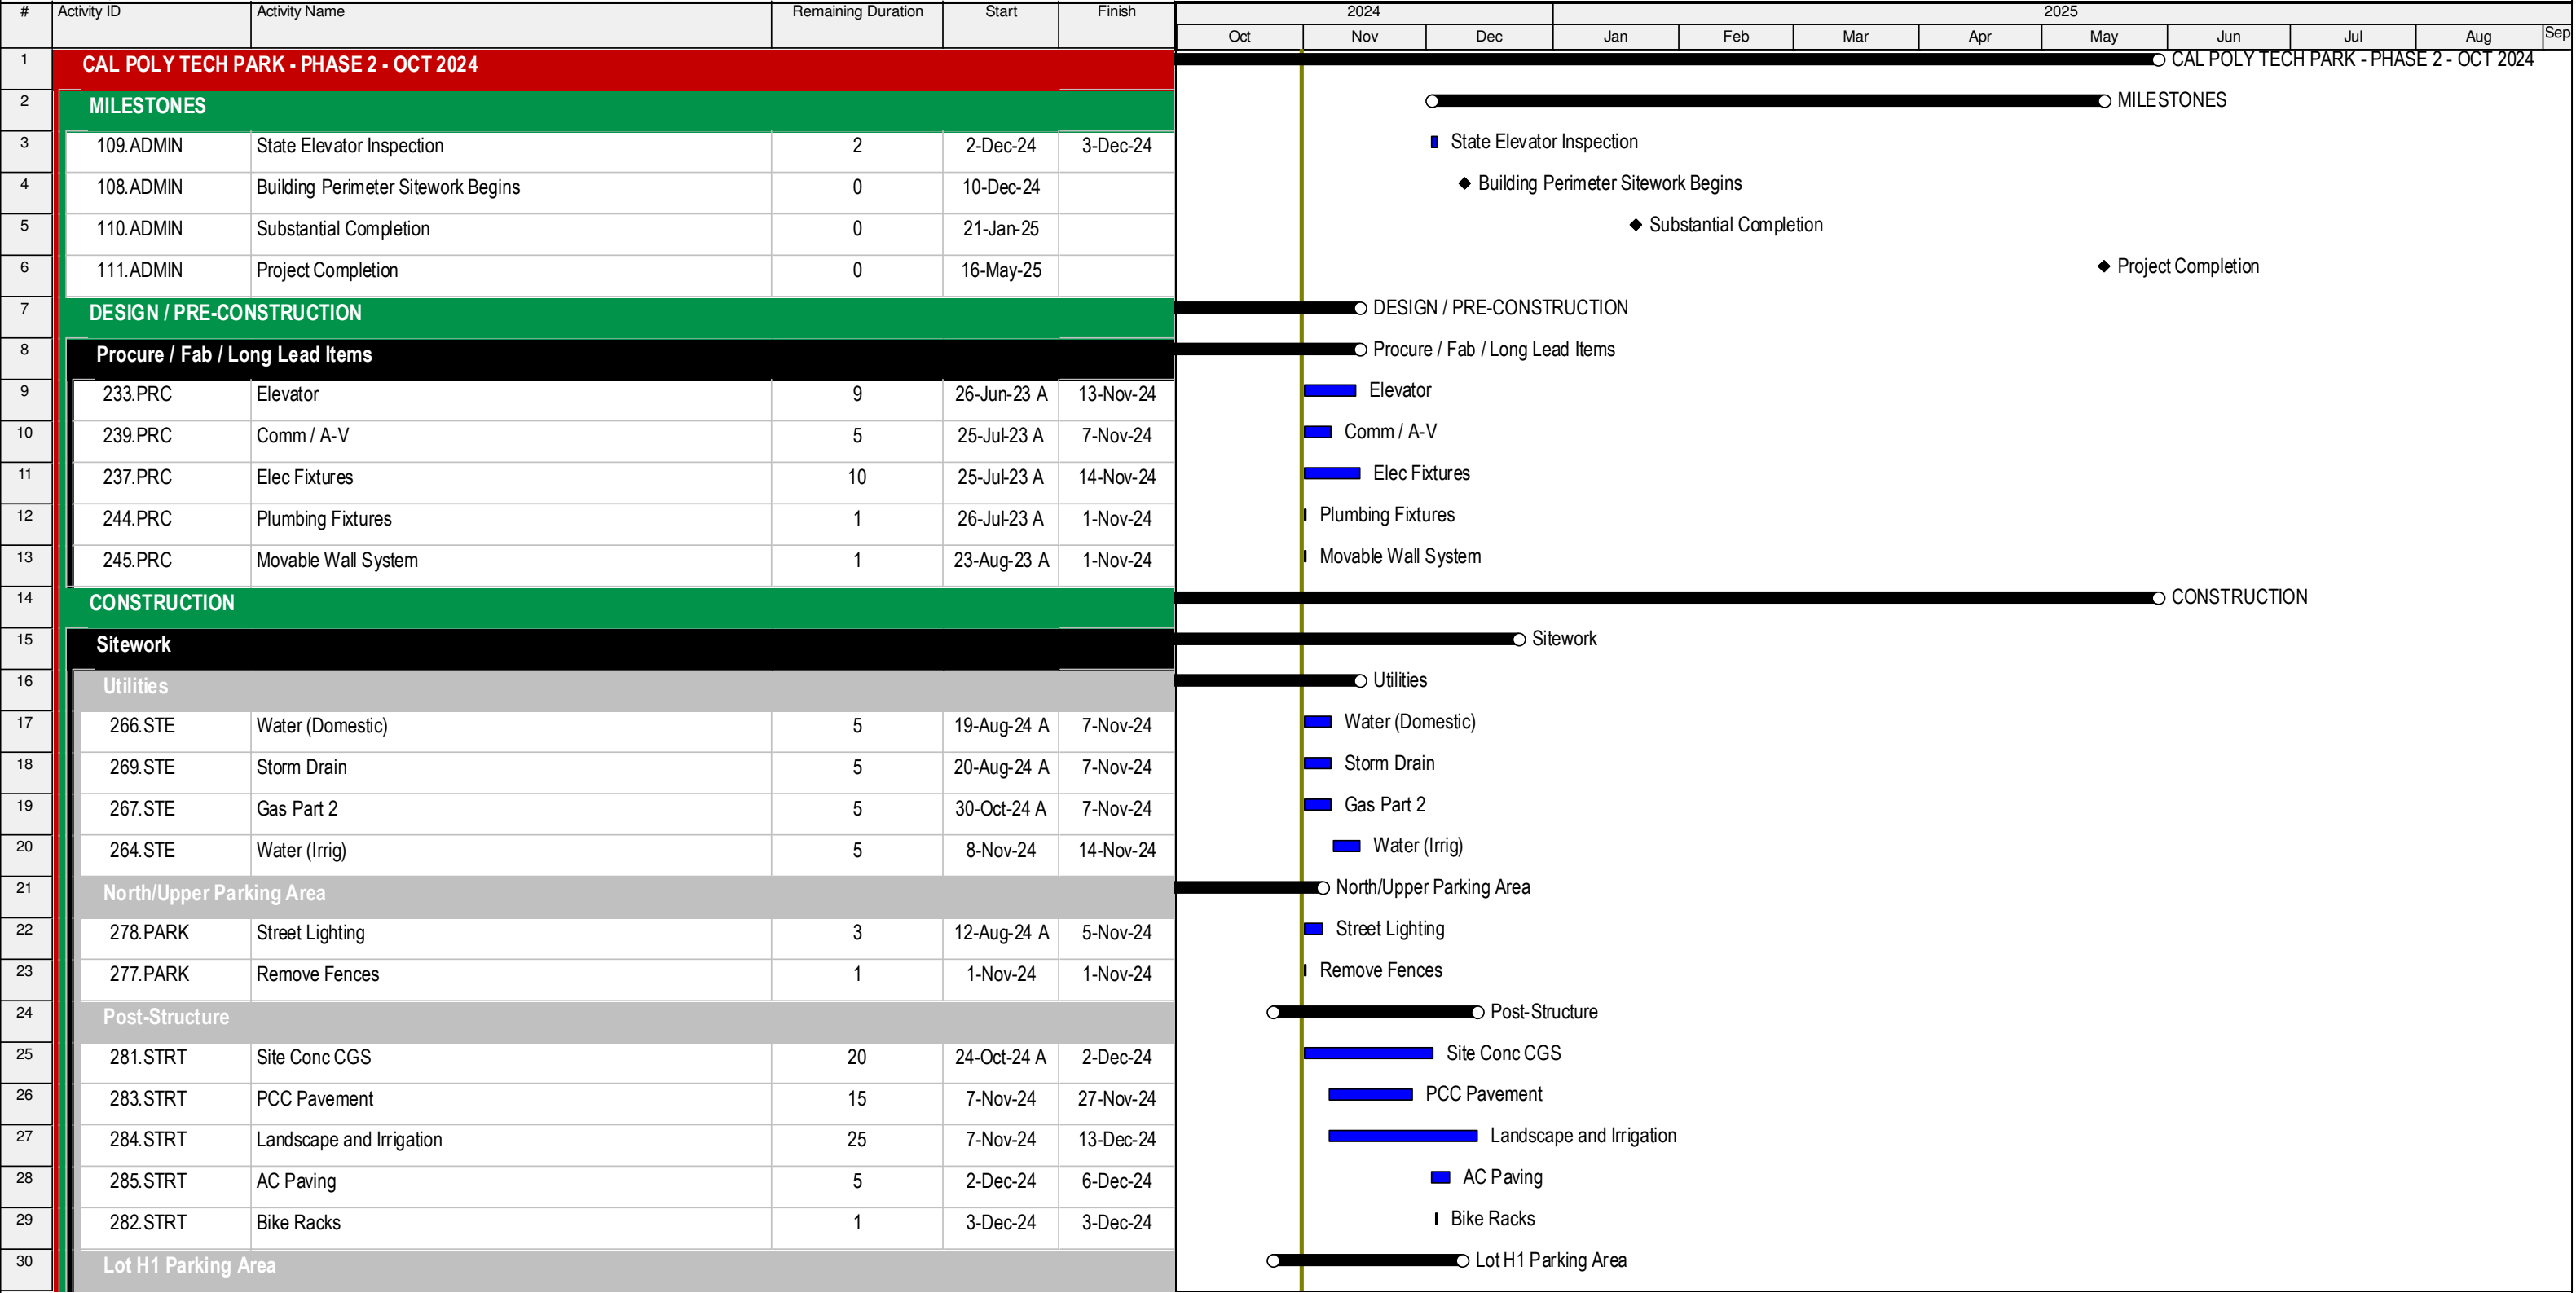

#	Activity ID	Activity Name	Remaining Duration	Start	Finish	2024			2025							
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
31	290.PRKLT	Pedestrian Bridge	15	24-Oct-24 A	21-Nov-24											
32	291.PRKLT	Concrete Stairs, Walkway	5	22-Nov-24	2-Dec-24											
33	292.PRKLT	Handrails	3	3-Dec-24	5-Dec-24											
34	293.PRKLT	Wheelstops	1	6-Dec-24	6-Dec-24											
35	294.PRKLT	Striping / Signage	1	9-Dec-24	9-Dec-24											
36	Bioretention Basin															
37	299.1.BASIN	Remove Jobsite Trailer	5	15-Nov-24	21-Nov-24											
38	296.BASIN	SWPPP / BMP's	2	10-Dec-24	11-Dec-24											
39	297.BASIN	Rough Grading	3	12-Dec-24	16-Dec-24											
40	298.BASIN	8" SD from Basin to Existing	3	17-Dec-24	19-Dec-24											
41	299.BASIN	Fine Grading	2	20-Dec-24	23-Dec-24											
42	Building															
43	Shell / Exterior															
44	Exterior Walls															
45	341.EXTWLL	Storefront Frames	10	12-Aug-24 A	14-Nov-24											
46	339.EXTWLL	Sheet Metal Flashing	10	23-Aug-24 A	14-Nov-24											
47	340.EXTWLL	Waterproof Membrane	10	26-Aug-24 A	14-Nov-24											
48	344.EXTWLL	Win / Strfrt Glazing / Hdwe	10	2-Sep-24 A	2-Dec-24											
49	342.EXTWLL	Metal Wall Panels	20	16-Sep-24 A	2-Dec-24											
50	346.EXTWLL	Exterior Wall Louvers	2	1-Nov-24	4-Nov-24											
51	343.EXTWLL	Ext HM Drs / Hdwe	5	3-Dec-24	9-Dec-24											
52	345.EXTWLL	Gutters / Downspouts	10	3-Dec-24	16-Dec-24											
53	Roof System															
54	351.ROOF	Standing Seam Metal Roof	4	9-Sep-24 A	6-Nov-24											
55	Roof Well / MEP															
56	354.RFMEP	Roof Hatch	1	1-Nov-24	1-Nov-24											
57	356.RFMEP	Electrical Connection to HVAC Units	2	1-Nov-24	4-Nov-24											
58	355.RFMEP	PVC Roof System	5	4-Nov-24	8-Nov-24											
59	358.RFMEP	Set HVAC Units / Ductwork Connection	3	11-Nov-24	13-Nov-24											
60	357.RFMEP	Connect Plumbing to HVAC Units	2	14-Nov-24	15-Nov-24											

- Remaining Level of Effort
- Remaining Work
- Critical Work
- Milestone
- Summary

CONSTRUCTION SCHEDULE - OCT 2024
SUBCONTRACTORS - REMAINING



#	Activity ID	Activity Name	Remaining Duration	Start	Finish	2024			2025											
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep			
61	Elevator					Elevator														
62	367.ELEV	SFM Inspection	1	1-Nov-24	1-Nov-24	SFM Inspection														
63	363.ELEV	Set Guide Rails	5	14-Nov-24	20-Nov-24	Set Guide Rails														
64	364.ELEV	Set Jacks	5	14-Nov-24	20-Nov-24	Set Jacks														
65	366.ELEV	Hall Call / Controls	5	21-Nov-24	27-Nov-24	Hall Call / Controls														
66	365.ELEV	Construct Cab	10	21-Nov-24	6-Dec-24	Construct Cab														
67	Interior Buildout					Interior Buildout														
68	377.INT	Gypsum Board / Tape / Finish	22	22-Jul-24 A	4-Dec-24	Gypsum Board / Tape / Finish														
69	386.INT	Finish HVAC	10	15-Sep-24 A	14-Nov-24	Finish HVAC														
70	378.INT	Paint	10	1-Nov-24	14-Nov-24	Paint														
71	371.INT	Movable Wall Support System	10	4-Nov-24	15-Nov-24	Movable Wall Support System														
72	379.INT	FRP	2	15-Nov-24	18-Nov-24	FRP														
73	384.INT	Fire Ext / Cabinets	3	15-Nov-24	19-Nov-24	Fire Ext / Cabinets														
74	380.INT	Plam Cabs / Countertop	5	15-Nov-24	21-Nov-24	Plam Cabs / Countertop														
75	391.INT	Ceiling Tile Install	5	15-Nov-24	21-Nov-24	Ceiling Tile Install														
76	390.INT	Signage	5	15-Nov-24	21-Nov-24	Signage														
77	382.INT	Finish Plumbing	10	15-Nov-24	2-Dec-24	Finish Plumbing														
78	381.INT	Ceiling Grid	15	15-Nov-24	9-Dec-24	Ceiling Grid														
79	385.INT	Firestopping	10	22-Nov-24	9-Dec-24	Firestopping														
80	383.INT	Finish Fire Spklr Sys	20	4-Dec-24	2-Jan-25	Finish Fire Spklr Sys														
81	387.INT	Finish Elec	10	10-Dec-24	23-Dec-24	Finish Elec														
82	388.INT	Carpet / Resilient Flrg	10	18-Dec-24	2-Jan-25	Carpet / Resilient Flrg														
83	389.INT	Sealed / Stained Concrete	5	26-Dec-24	2-Jan-25	Sealed / Stained Concrete														
84	Bathrooms - 1st Floor					Bathrooms - 1st Floor														
85	397.1STBATH	Gypsum Board	12	26-Aug-24 A	18-Nov-24	Gypsum Board														
86	398.1STBATH	Paint	10	19-Nov-24	4-Dec-24	Paint														
87	399.1STBATH	Tile	5	5-Dec-24	11-Dec-24	Tile														
88	400.1STBATH	Finish HVAC	5	12-Dec-24	18-Dec-24	Finish HVAC														
89	401.1STBATH	Finish Plbg	10	12-Dec-24	26-Dec-24	Finish Plbg														
90	402.1STBATH	Finish Elec	5	19-Dec-24	26-Dec-24	Finish Elec														

- Remaining Level of Effort
- Remaining Work
- Critical Work
- ◆ Milestone
- Summary

CONSTRUCTION SCHEDULE - OCT 2024
SUBCONTRACTORS - REMAINING



- CONSTRUCTION SCHEDULE - OCT 2024**
SUBCONTRACTORS - REMAINING

PAGE 4 of 6
DATA DATE:31-Oct-24
RUN DATE: 14-Nov-24 / 14:50




#	Activity ID	Activity Name	Remaining Duration	Start	Finish	2024			2025										
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep		
121	507.INSP	Fire Sprinkler System Piping / Earthquake Bracing 2nd Floor	0		31-Oct-24	◆ Fire Sprinkler System Piping / Earthquake Bracing 2nd Floor													
122	Mechanical Systems					○ Mechanical Systems													
123	509.INSP	Fire and or Smoke Dampers	0		27-Jan-25	◆ Fire and or Smoke Dampers													
124	510.INSP	HVAC System Shutdown	0		27-Jan-25	◆ HVAC System Shutdown													
125	Fire Alarm Systems					○ Fire Alarm Systems													
126	511.INSP	Fire Alarm System Testing	0		27-Jan-25	◆ Fire Alarm System Testing													
127	512.INSP	Fire Sprinkler System Piping Flow Test	0		27-Jan-25	◆ Fire Sprinkler System Piping Flow Test													
128	Special Requirements					○ Special Requirements													
129	513.INSP	Elevators	0		18-Dec-24	◆ Elevators													
130	514.INSP	Electrical / Generator / Photovoltaic / UPS	0		27-Jan-25	◆ Electrical / Generator / Photovoltaic / UPS													
131	Punchlist					○ Punchlist													
132	428.PUNCH	Punchlist	10	7-Jan-25	20-Jan-25	Punchlist													
133	2nd Floor Tenant Improvement					○ 2nd Floor Tenant Improvement													
134	551.PCO	Metal Stud Framing	25	1-Nov-24	9-Dec-24	Metal Stud Framing													
135	552.PCO	Rough Plumbing	7	3-Dec-24	11-Dec-24	Rough Plumbing													
136	553.PCO	Rough Electrical	25	3-Dec-24	8-Jan-25	Rough Electrical													
137	554.PCO	Rough HVAC	10	10-Dec-24	23-Dec-24	Rough HVAC													
138	555.PCO	Rough Frame Inspection	1	23-Dec-24	23-Dec-24	Rough Frame Inspection													
139	556.PCO	Gyp Board One Side	8	9-Jan-25	20-Jan-25	Gyp Board One Side													
140	557.PCO	Insulation	2	21-Jan-25	22-Jan-25	Insulation													
141	558.PCO	Insulation Inspection	1	23-Jan-25	23-Jan-25	Insulation Inspection													
142	559.PCO	Complete Gyp Board Installation	15	23-Jan-25	12-Feb-25	Complete Gyp Board Installation													
143	560.PCO	Dyrwall Nailing Inspection	1	13-Feb-25	13-Feb-25	Dyrwall Nailing Inspection													
144	561.PCO	Storefront Frames	5	13-Feb-25	19-Feb-25	Storefront Frames													
145	562.PCO	Tape & Finish Gyp Board	20	13-Feb-25	12-Mar-25	Tape & Finish Gyp Board													
146	563.PCO	Interior Paint	10	6-Mar-25	19-Mar-25	Interior Paint													
147	564.PCO	Complete Punch List	10	6-Mar-25	19-Mar-25	Complete Punch List													
148	565.PCO	Fire Sprinkler Drops	5	13-Mar-25	19-Mar-25	Fire Sprinkler Drops													
149	566.PCO	T-Bar Ceiling	4	14-Mar-25	19-Mar-25	T-Bar Ceiling													
150	567.PCO	Casework & Counter Tops	2	19-Mar-25	20-Mar-25	Casework & Counter Tops													

- Remaining Level of Effort
- Remaining Work
- Critical Work
- ◆ Milestone
- Summary

CONSTRUCTION SCHEDULE - OCT 2024
SUBCONTRACTORS - REMAINING



#	Activity ID	Activity Name	Remaining Duration	Start	Finish	2024			2025								
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
151	568.PCO	Finish Plumbing	5	20-Mar-25	26-Mar-25												
152	569.PCO	Finish Fire Sprinklers	5	20-Mar-25	26-Mar-25												
153	570.PCO	Finish HVAC	15	20-Mar-25	9-Apr-25												
154	571.PCO	Finish Electrical	15	20-Mar-25	9-Apr-25												
155	572.PCO	Above Ceiling & SFM Inspection	1	9-Apr-25	9-Apr-25												
156	573.PCO	Drop Ceiling Tiles	2	10-Apr-25	11-Apr-25												
157	574.PCO	HVAC Equipment Start Up	10	10-Apr-25	23-Apr-25												
158	575.PCO	Flooring, Carpet and Base	5	14-Apr-25	18-Apr-25												
159	576.PCO	Seal Concrete	2	21-Apr-25	22-Apr-25												
160	577.PCO	Polish Concrete Floors	10	23-Apr-25	6-May-25												
161	578.PCO	Testing & Air Balancing	5	24-Apr-25	30-Apr-25												
162	579.PCO	Punch List Inspection	1	1-May-25	1-May-25												
163	580.PCO	Fire Alarm Testing	5	1-May-25	7-May-25												
164	581.PCO	State Fire Marshall Final Inspections	20	1-May-25	29-May-25												
165	582.PCO	Complete Punchlist	10	2-May-25	15-May-25												

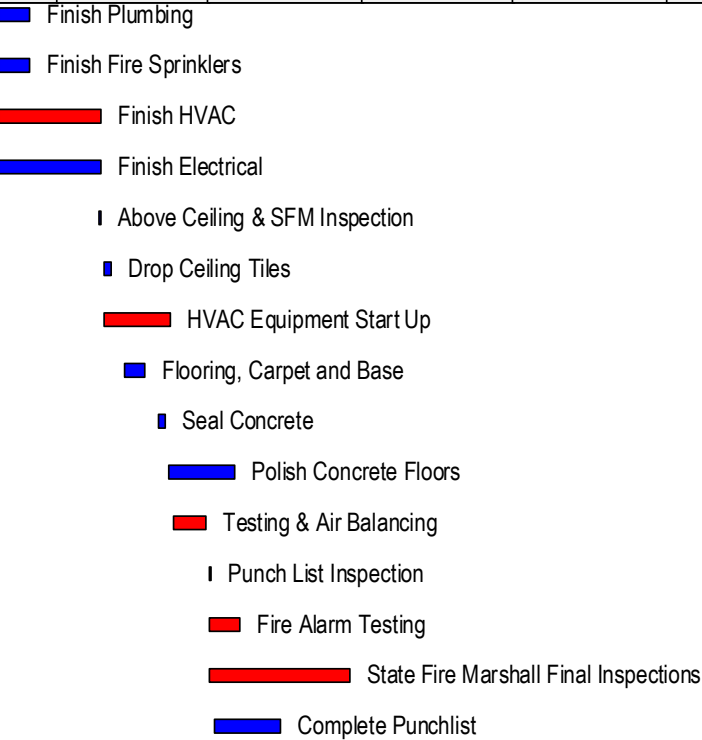

- Remaining Level of Effort
- Remaining Work
- Critical Work
- Milestone
- Summary

CONSTRUCTION SCHEDULE - OCT 2024
SUBCONTRACTORS - REMAINING
