


Activity ID	Activity Name	OrigDur	RemDur	Start	Finish	Phy %	Total Fical	2021												2022												2023												2024	
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb				
Total		576d	340d	21-Apr-21 A	09-Aug-23		-124d	09-Aug-23, Total																																					
FY18 - GROUND TRANSPORT EQUIPMENT FACILITY - INITIAL SCHEDULE ORG -22 0413		576d	340d	21-Apr-21 A	09-Aug-23		-124d	09-Aug-23, FY18 - GROUND TRANSPORT EQUIPMENT																																					
MILESTONES		576d	71d	21-Apr-21 A	09-Aug-23		-124d	09-Aug-23, MILESTONES																																					
NTP-100	NTP EXECUTED	0d	0d	21-Apr-21 A		100%		NTP EXECUTED																																					
0004	Payment and Performance Bond	5d	0d	21-Apr-21 A	27-Apr-21 A	100%		Payment and Performance Bond																																					
MILE-210	Substantial Completion	0d	0d		27-Apr-23	0%	-53d	◆ Substantial Completion																																					
MILE-200	End Project	0d	0d		09-Aug-23*	0%	-124d	◆ End Project																																					
MODIFICATIONS		62d	34d	16-Nov-21 A	18-May-22		107d	18-May-22, MODIFICATIONS																																					
MOD-500	Termite Control	5d	3d	16-Nov-21 A	05-Apr-22	75%	1d	Termite Control																																					
MOD-510	POC of 2 Water Lines	5d	0d	10-Mar-22 A	21-Mar-22 A	100%		POC of 2 Water Lines																																					
SITE-740	CLIN 4 Mod- SS MH H-3 to H-4 8"	5d	0d	21-Mar-22 A	22-Mar-22 A	100%		CLIN 4 Mod- SS MH H-3 to H-4 8"																																					
RFP 2,5,7		20d	20d	07-Apr-22	04-May-22		117d	04-May-22, RFP 2,5,7																																					
MOD-700	Install RFP 2, 5, and 7	20d	20d	07-Apr-22	04-May-22	0%	117d	Install RFP 2, 5, and 7																																					
RFP-6 Utilities Added Future Use		9d	9d	13-Apr-22	25-Apr-22		19d	25-Apr-22, RFP-6 Utilities Added Future Use																																					
MOD-800	Install Utilities for Future Use	9d	9d	13-Apr-22	25-Apr-22	0%	19d	Install Utilities for Future Use																																					
Mod- Comm Vault & Water Line		15d	15d	26-Apr-22	18-May-22		17d	18-May-22, Mod- Comm Vault & Water Line																																					
MOD-900	Comm Vault and Water Line	15d	15d	26-Apr-22	18-May-22	0%	17d	Comm Vault and Water Line																																					
Mod- Electrical Room Door Setup		10d	10d	01-Apr-22	14-Apr-22		131d	14-Apr-22, Mod- Electrical Room Door Setup																																					
MOD-1000	Electrical Room Door Setup	10d	10d	01-Apr-22	14-Apr-22	0%	131d	Electrical Room Door Setup																																					
DESIGN PHASE		451d	340d	21-Apr-21 A	09-Aug-23		-124d	09-Aug-23, DESIGN PHASE																																					
GN-120	General Conditions	660d	496d	21-Apr-21 A	09-Aug-23	64%	-180d	General Conditions																																					
GN-110	Bonding / Insurance	5d	5d	21-Apr-21 A	07-Apr-22	20%	-45d	Bonding / Insurance																																					
PRELIMINARY SCHEDULE SUBMITTALS		128d	25d	21-Apr-21 A	05-May-22		185d	05-May-22, PRELIMINARY SCHEDULE SUBMITTALS																																					
SD-01 SUBMITTALS		128d	25d	21-Apr-21 A	05-May-22		185d	05-May-22, SD-01 SUBMITTALS																																					
Submittal Development		128d	25d	21-Apr-21 A	05-May-22		185d	05-May-22, Submittal Development																																					
SUB-150	Submit Certificate of Ins.	5d	0d	21-Apr-21 A	21-Apr-21 A	100%		Submit Certificate of Ins.																																					
SUB-100	Submit APP	5d	0d	14-May-21 A	14-May-21 A	100%		Submit APP																																					
SUB-110	Submit CQCP	5d	0d	14-May-21 A	14-May-21 A	100%		Submit CQCP																																					
SUB-210	Submit Health Haz Control Plan	5d	0d	14-May-21 A	14-May-21 A	100%		Submit Health Haz Control Plan																																					
SUB-220	Submit Emergency Action Plan	5d	0d	14-May-21 A	14-May-21 A	100%		Submit Emergency Action Plan																																					
SUB-250	Submit AHA's	5d	2d	14-May-21 A	04-Apr-22	50%	17d	Submit AHA's																																					
SUB-140	Submit WMP	5d	0d	17-May-21 A	17-May-21 A	100%		Submit WMP																																					
SUB-190	Submit Submittal Register	5d	0d	17-May-21 A	17-May-21 A	100%		Submit Submittal Register																																					
SUB-120	Submit Construction Site Plan	5d	0d	19-May-21 A	19-May-21 A	100%		Submit Construction Site Plan																																					
SUB-130	Submit EPP	5d	0d	24-May-21 A	24-May-21 A	100%		Submit EPP																																					
SUB-320	Submit 015723-SWPPP	5d	0d	24-May-21 A	24-May-21 A	100%		Submit 015723-SWPPP																																					
SUB-330	Submit 015723-PRR	5d	0d	07-Jun-21 A	07-Jun-21 A	100%		Submit 015723-PRR																																					
SUB-710	Submit 310000- Shoring	5d	0d	09-Jun-21 A	14-Jun-21 A	100%		Submit 310000- Shoring																																					
SUB-720	Submit 310000- Dewatering WP	5d	0d	09-Jun-21 A	14-Jun-21 A	100%		Submit 310000- Dewatering WP																																					
SUB-750	Submit 333000- Existing Cond.	5d	0d	15-Jul-21 A	21-Jul-21 A	100%		Submit 333000- Existing Cond.																																					
SUB-760	Submit 333000- Req Fid Support	5d	0d	15-Jul-21 A	21-Jul-21 A	100%		Submit 333000- Req Fid Support																																					
SUB-770	Submit 333000- Preinsp Conn.	5d	0d	15-Jul-21 A	21-Jul-21 A	100%		Submit 333000- Preinsp Conn.																																					
SUB-260	Submit 014500-MTC Validation	5d	0d	23-Jul-21 A	23-Jul-21 A	100%		Submit 014500-MTC Validation																																					
SUB-1000	Submit Div 26 Submittals	5d	0d	06-Aug-21 A	06-Aug-21 A	100%		Submit Div 26 Submittals																																					
SUB-410	Submit 033000-Lab Accred.	5d	0d	12-Aug-21 A	12-Aug-21 A	100%		Submit 033000-Lab Accred.																																					
SUB-180	Submit Initial Schedule	5d	0d	17-Aug-21 A	17-Aug-21 A	100%		Submit Initial Schedule																																					
SUB-880	Submit Div 5 [NonPEMB]	5d	0d	12-Sep-21 A	14-Sep-21 A	100%		Submit Div 5 [NonPEMB]																																					
SUB-500	Submit 134856-Bridge Manf Qual	5d	0d	29-Sep-21 A	29-Sep-21 A	100%		Submit 134856-Bridge Manf Qual																																					
SUB-1005	Submit Div 23 Submittals	5d	0d	30-Sep-21 A	30-Sep-21 A	100%		Submit Div 23 Submittals																																					
SUB-400	Submit 033000-QCP	5d	0d	07-Oct-21 A	12-Oct-21 A	100%		Submit 033000-QCP																																					
SUB-420	Submit 033000-Sampling Plan	5d	0d	07-Oct-21 A	07-Oct-21 A	100%		Submit 033000-Sampling Plan																																					
SUB-430	Submit 034213-Qual Control Prc	5d	0d	07-Oct-21 A	07-Oct-21 A	100%		Submit 034213-Qual Control Prc																																					
SUB-840	Submit Fire Protection Spec.	5d	0d	14-Oct-21 A	14-Oct-21 A	100%		Submit Fire Protection Spec.																																					
SUB-560	Submit 230515- M,E,F List	5d	0d	27-Oct-21 A	28-Oct-21 A	100%		Submit 230515- M,E,F List																																					
SUB-580	Submit 230593- TAB Firm	5d	0d	17-Nov-21 A	17-Nov-21 A	100%		Submit 230593- TAB Firm																																					
SUB-590	Submit 230593-TAB Team Assist.	5d	0d	17-Nov-21 A	17-Nov-21 A	100%		Submit 230593-TAB Team Assist.																																					
SUB-600	Submit 230593- TAB Team Eng.	5d	0d	17-Nov-21 A	17-Nov-21 A	100%		Submit 230593- TAB Team Eng.																																					
SUB-450	Submit 051200- Erection Drawings	5d	0d	01-Dec-21 A	01-Dec-21 A	100%		Submit 051200- Erection Drawings																																					
SUB-230	Submit Standard Lift Plan	5d	0d	08-Dec-21 A	08-Dec-21 A	100%		Submit Standard Lift Plan																																					
SUB-240	Submit Critical Lift Plan	5d	0d	08-Dec-21 A	08-Dec-21 A	100%		Submit Critical Lift Plan																																					
SUB-510	Submit 134856-Manf Tech Lit	5d	0d	08-Dec-21 A	08-Dec-21 A	100%		Submit 134856-Manf Tech Lit																																					
SUB-520	Submit 134856- Manf Design	5d	0d	08-Dec-21 A	08-Dec-21 A	100%		Submit 134856- Manf Design																																					
SUB-530	Submit 134856- Rep Design Calc	5d	0d	08-Dec-21 A	08-Dec-21 A	100%		Submit 134856- Rep Design Calc																																					
SUB-540	Submit 134856- Splice Proc.	5d	0d	08-Dec-21 A	08-Dec-21 A	100%		Submit 134856- Splice Proc.																																					
SUB-550	Submit 134856- Welder Quals	5d	0d	08-Dec-21 A	08-Dec-21 A	100%		Submit 134856- Welder Quals																																					
SUB-200	Submit HP&Sust. Bldg Chklist	5d	0d	09-Dec-21 A	14-Jan-22 A	100%		Submit HP&Sust. Bldg Chklist																																					
SUB-300	Submit 015000-Temp Erthwrk Pln	5d	0d	12-Dec-21 A	12-Dec-21 A	100%		Submit 015000-Temp Erthwrk Pln																																					
SUB-690	Submit 271323- Qualifications	5d	0d	18-Dec-21 A	18-Dec-21 A	100%		Submit 271323- Qualifications																																					
SUB-1010	Submit Div 8 Submittals	5d	2d	16-Feb-22 A	04-Apr-22	60%	20d	Submit Div 8 Submittals																																					
SUB-440	Submit 050523.16- Welding QAP	5d	0d	24-Feb-22 A	08-Mar-22 A	100%		Submit 050523.16- Welding QAP																																					
SUB-310	Submit 015000-Dust Control Pln	5d	0d	01-Mar-22 A	07-Mar-22 A	100%		Submit 015000-Dust Control Pln																																					
SUB-460	Submit 52100- Welder Qual	5d	0d	24-Mar-22 A	31-Mar-22 A	100%		Submit 52100- Welder Qual																																					


█ Actual Work █ Critical Remaining Work
█ Remaining Work ◆ Milestone

Banded Schedule

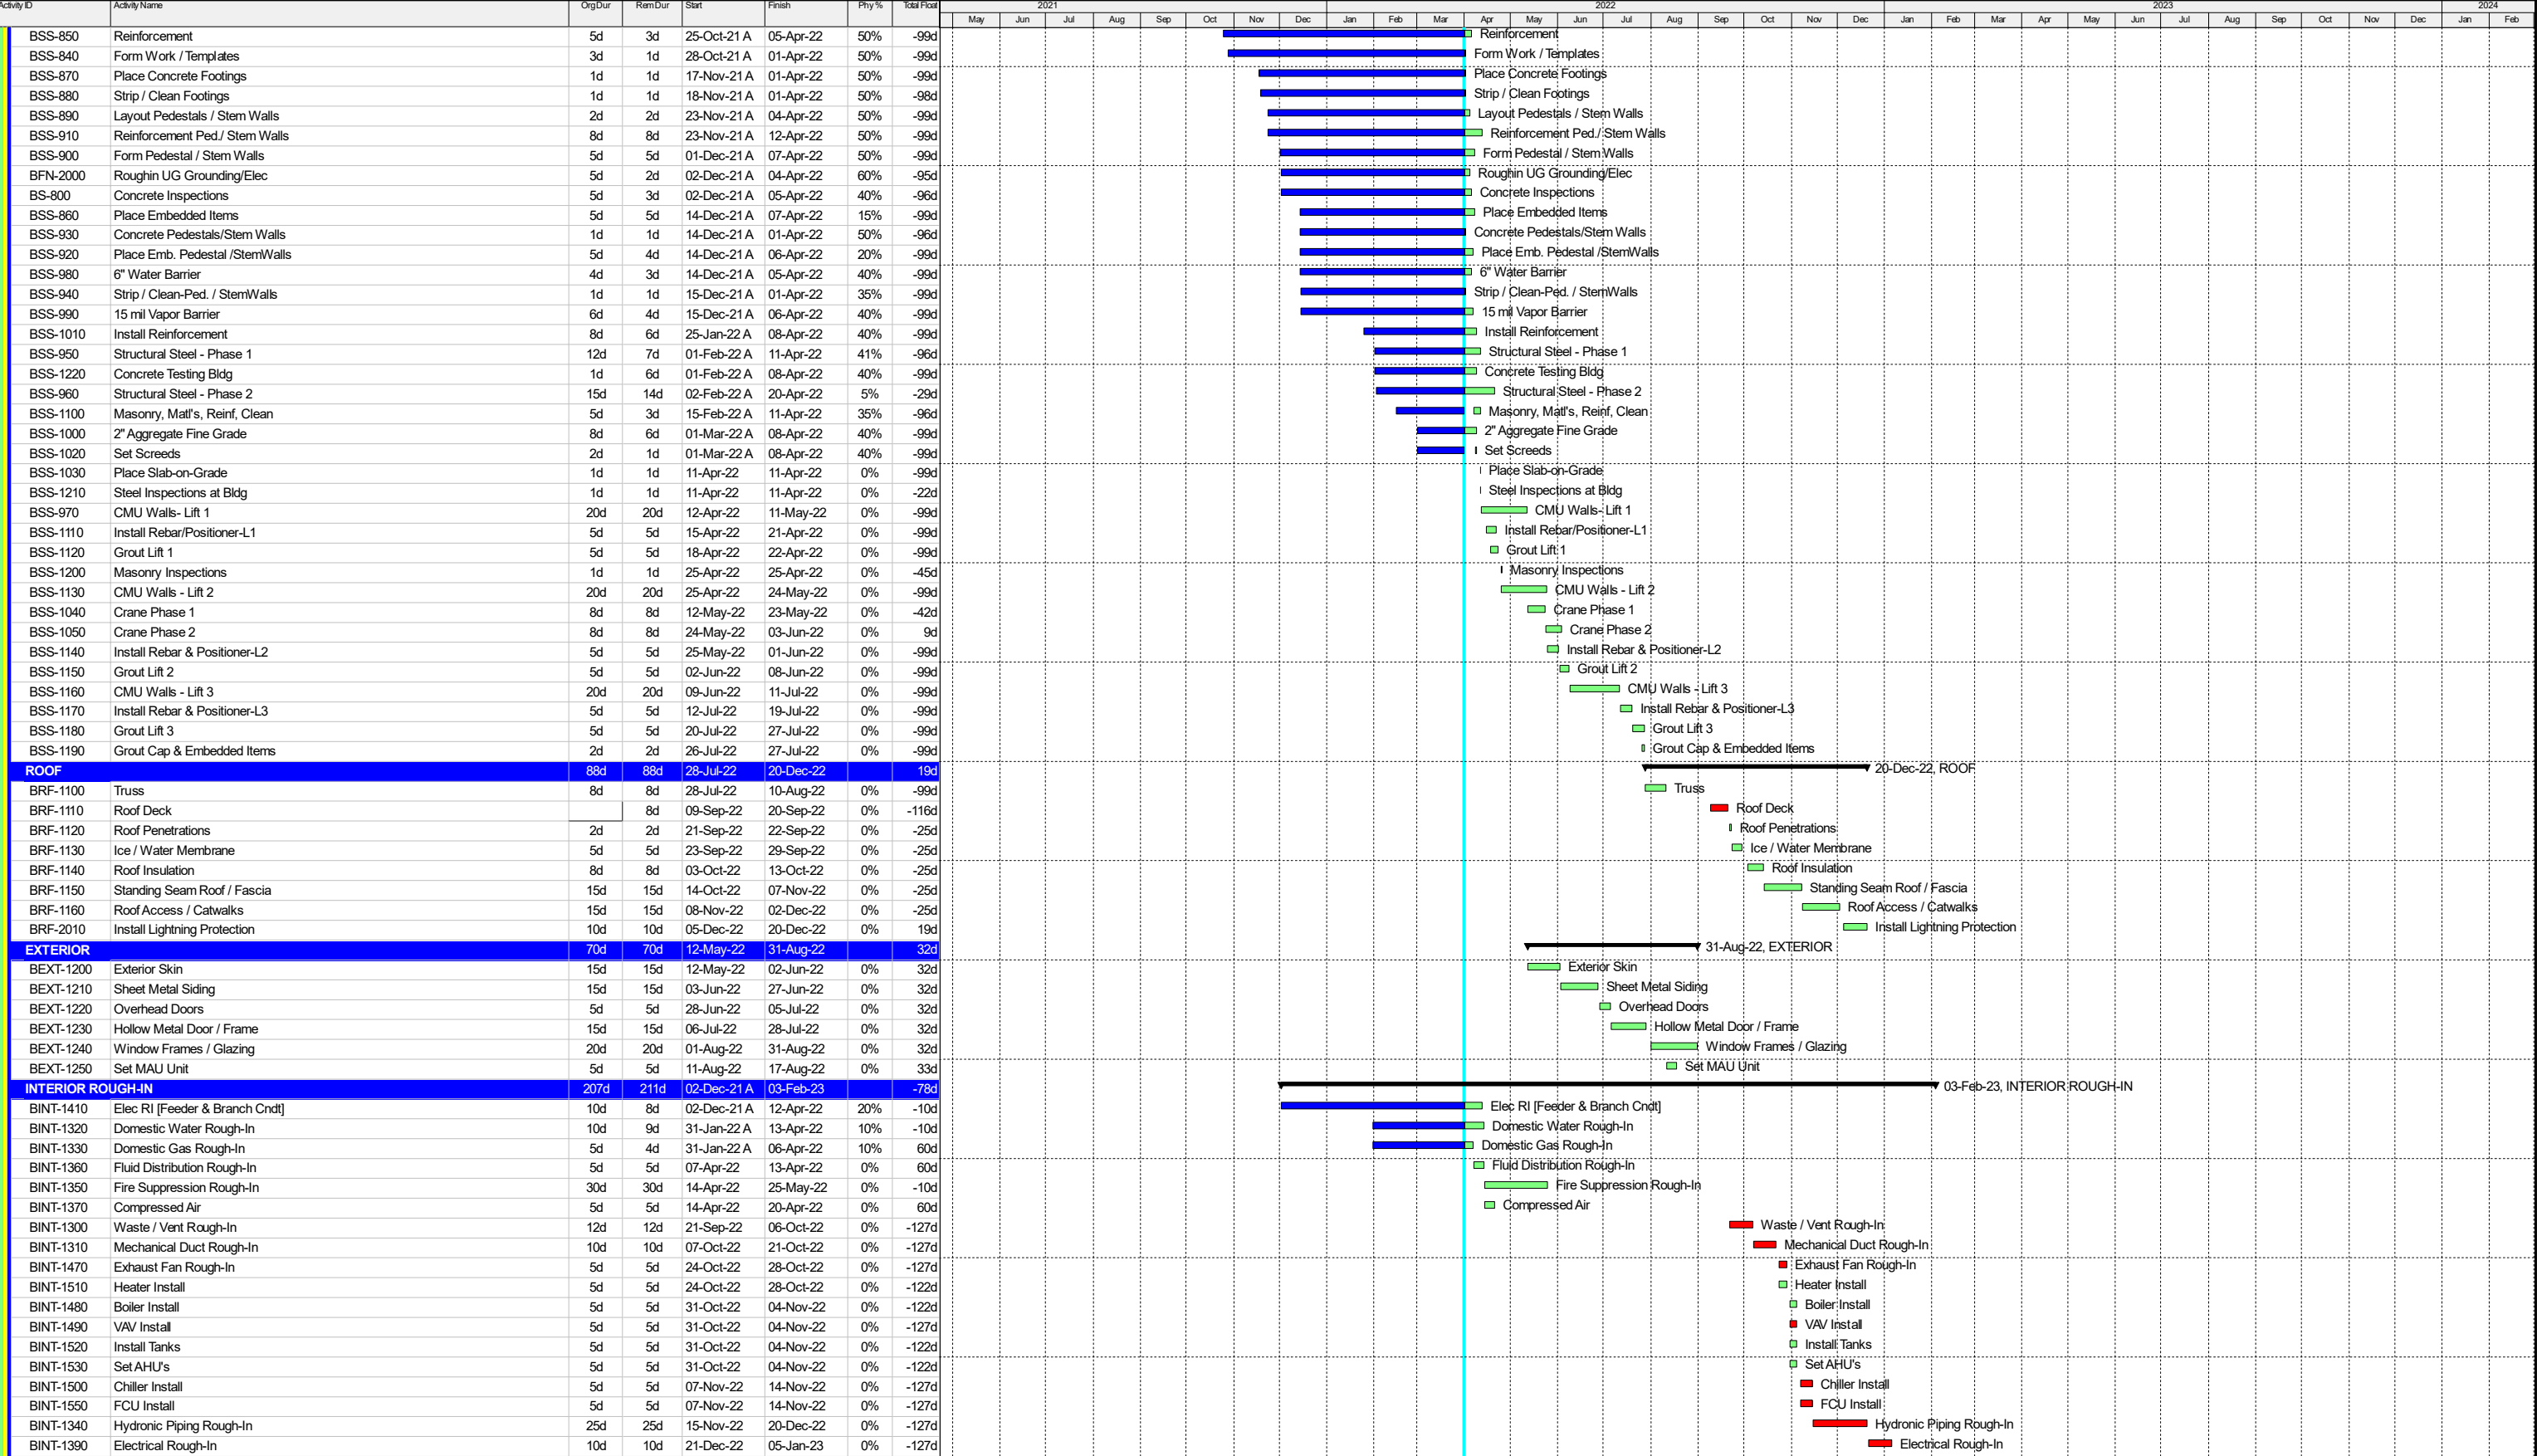

█ Actual Work █ Critical Remaining Work
█ Remaining Work ◆ Milestone

Banded Schedule

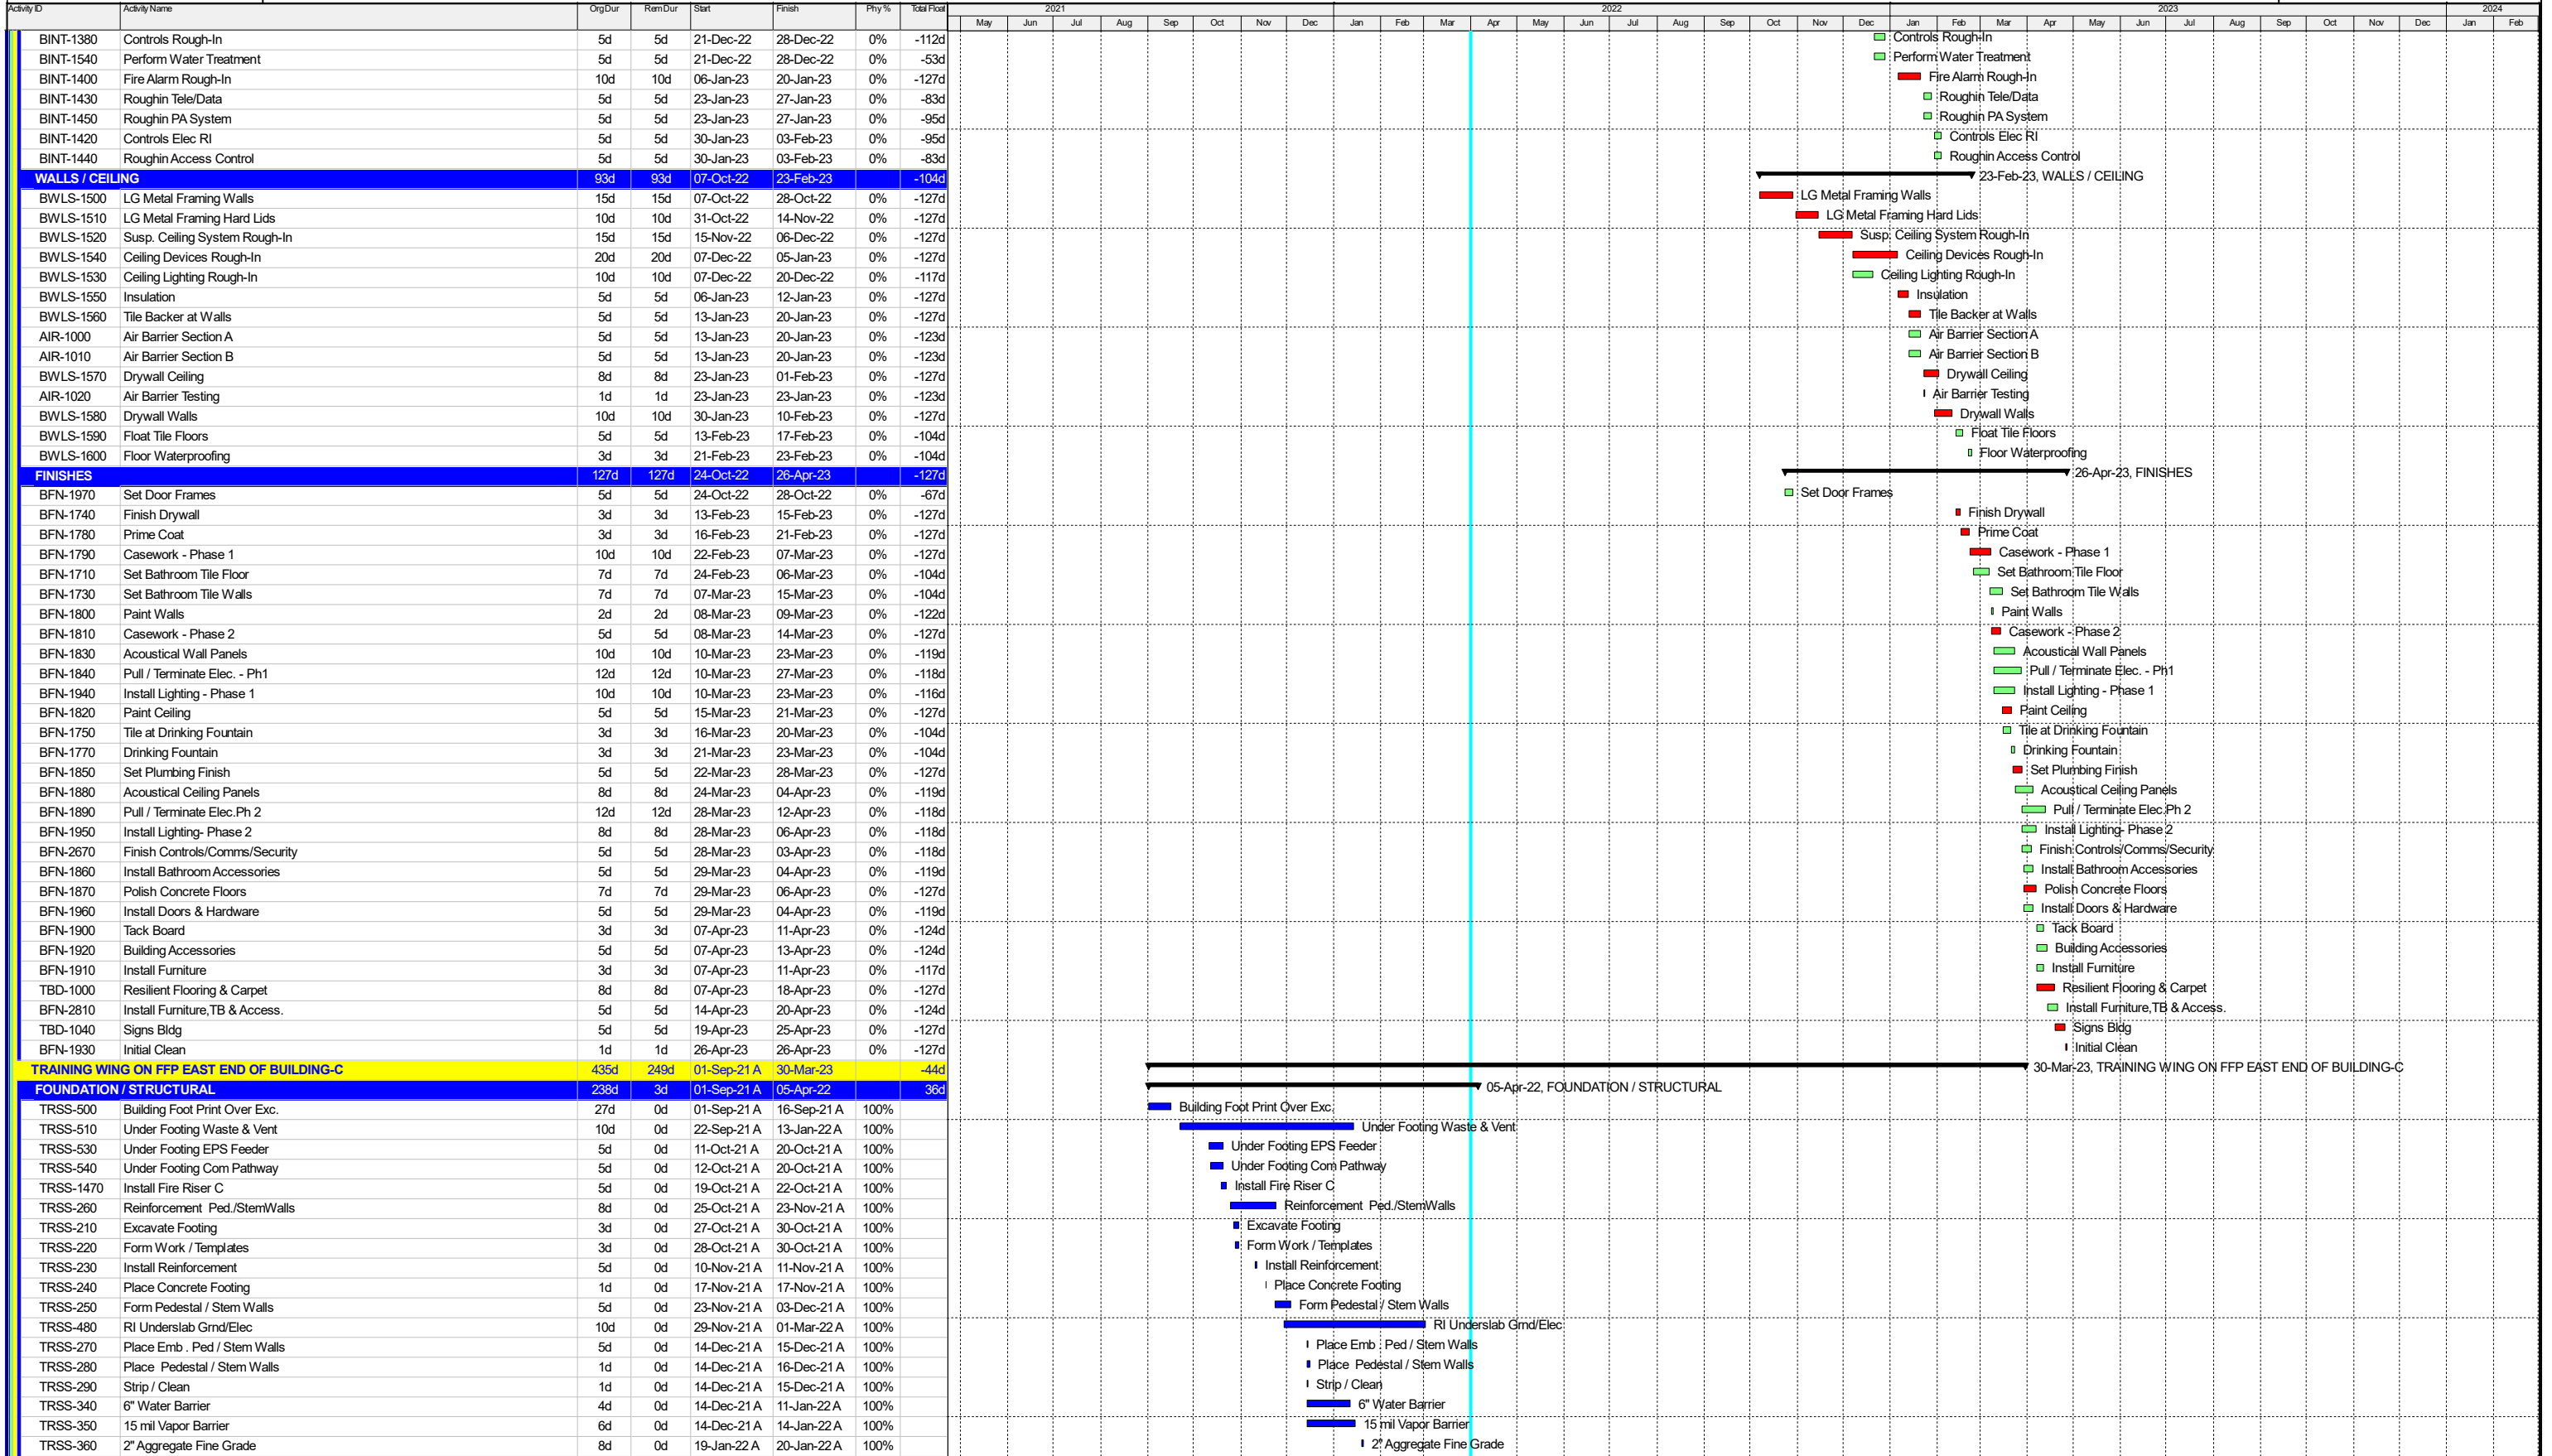

■ Actual Work ■ Critical Remaining Work
■ Remaining Work ◆ Milestone

Banded Schedule

