

#	Activity ID	Activity Name	Original Duration	% Complete	Start	Finish	Total Float	2024												2025							
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
1	<b>ALHAMBRA - SAN GABRIEL HS NEW VEHICLE MAINTENANCE FACILITY</b>		168		13-Feb-24	09-Oct-24	0	○ 09-Oct-24, ALHAMBRA - SAN GABRIEL HS NEW VEHICLE MAINTENANCE FACILITY																			
2	<b>ADMIN</b>		168		13-Feb-24	09-Oct-24	0	○ 09-Oct-24, ADMIN																			
3	100.ADM	NOTICE TO PROCEED (2/13/24)	0	0%	13-Feb-24		0	◆ NOTICE TO PROCEED (2/13/24), 13-Feb-24																			
4	103.ADM	PROJECT DURATION	240	0%	13-Feb-24	09-Oct-24	0	PROJECT DURATION																			
5	101.ADM	PROJECT COMPLETION (10/9/24)	0	0%		09-Oct-24*	0	◆ PROJECT COMPLETION (10/9/24),																			
6	<b>CONSTRUCTION</b>		168		13-Feb-24	09-Oct-24	0	○ 09-Oct-24, CONSTRUCTION																			
7	<b>MOBILIZATION</b>		6		13-Feb-24	21-Feb-24	162	○ 21-Feb-24, MOBILIZATION																			
8	200.MOB	OFFICE TRAILER DELIVERY AND SET-UP	1	0%	13-Feb-24	13-Feb-24	4	OFFICE TRAILER DELIVERY AND SET-UP																			
9	201.MOB	MOBILIZATION	3	0%	13-Feb-24	15-Feb-24	0	MOBILIZATION																			
10	202.MOB	SWPPP / BMP's / EROSION CONTROL	1	0%	14-Feb-24	14-Feb-24	4	SWPPP / BMP's / EROSION CONTROL																			
11	205.MOB	INSTALL TEMP CHAIN LINK FENCE AND GATES	2	0%	16-Feb-24	20-Feb-24	0	INSTALL TEMP CHAIN LINK FENCE AND GATES																			
12	203.MOB	TEMP SIGNS, FEC'S, FIRST AID, SUPPLY	2	0%	16-Feb-24	20-Feb-24	163	TEMP SIGNS, FEC'S, FIRST AID, SUPPLY																			
13	204.MOB	TEMP POWER / TEMP WATER	3	0%	16-Feb-24	21-Feb-24	0	TEMP POWER / TEMP WATER																			
14	206.MOB	TELE/COMM EQUIPMENT AND CONNECTION	1	0%	21-Feb-24	21-Feb-24	0	TELE/COMM EQUIPMENT AND CONNECTION																			
15	<b>DEMOLITION</b>		13		22-Feb-24	11-Mar-24	0	○ 11-Mar-24, DEMOLITION																			
16	220.DEM	STAKE OUT EXISTING UG UTILITIES	2	0%	22-Feb-24	23-Feb-24	0	STAKE OUT EXISTING UG UTILITIES																			
17	221.DEM	SAFE-OFF & UTILITY CAP	2	0%	26-Feb-24	27-Feb-24	0	SAFE-OFF & UTILITY CAP																			
18	222.DEM	PROTECT IN PLACE (SHEET A1.01)	1	0%	28-Feb-24	28-Feb-24	1	PROTECT IN PLACE (SHEET A1.01)																			
19	223.DEM	REMOVE EXISTING UTILITIES (FIRE HYDRANT)	1	0%	28-Feb-24	28-Feb-24	3	REMOVE EXISTING UTILITIES (FIRE HYDRANT)																			
20	224.DEM	SITE DEMOLITION-CURBS ETC	2	0%	28-Feb-24	29-Feb-24	0	SITE DEMOLITION-CURBS ETC																			
21	225.DEM	SAWCUT	2	0%	01-Mar-24	04-Mar-24	0	SAWCUT																			
22	226.DEM	REMOVE AC AND REMOVE CONCRETE (A1.01)	2	0%	05-Mar-24	06-Mar-24	0	REMOVE AC AND REMOVE CONCRETE (A1.01)																			
23	227.DEM	CLEAR AND GRUB (A1.01)	1	0%	07-Mar-24	07-Mar-24	0	CLEAR AND GRUB (A1.01)																			
24	228.DEM	DEMO EXISTING UTILITIES	2	0%	08-Mar-24	11-Mar-24	0	DEMO EXISTING UTILITIES																			

█ Actual Level of Effort    ○ summary  
█ Actual Work  
█ Remaining Work  
█ Critical Remaining Work  
◆ Milestone

**BASELINE  
ALL**

Page 1 of 9  
 Data Date: 13-Feb-24  
 Run Date: 26-Jan-24 / 14:17






#	Activity ID	Activity Name	Original Duration	% Complete	Start	Finish	Total Float	2024												2025							
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
25	<b>BUILDING</b>		132		12-Mar-24	16-Sep-24	0	○ 16-Sep-24, BUILDING																			
26	<b>GRADING</b>		5		12-Mar-24	18-Mar-24	0	○ 18-Mar-24, GRADING																			
27	240.GRD	ROUGH GRADE	2	0%	12-Mar-24	13-Mar-24	0	■ ROUGH GRADE																			
28	241.GRD	OVER EXCAVATE / COMPACT / FINE GRADE	2	0%	14-Mar-24	15-Mar-24	0	■ OVER EXCAVATE / COMPACT / FINE GRADE																			
29	242.GRD	CERTIFY PAD	1	0%	18-Mar-24	18-Mar-24	0	CERTIFY PAD																			
30	<b>UG UTILITIES</b>		7		19-Mar-24	27-Mar-24	0	○ 27-Mar-24, UG UTILITIES																			
31	250.UTL	U/G MEPF	5	0%	19-Mar-24	25-Mar-24	0	■ U/G MEPF																			
32	251.UTL	U/G TRENCH DRAIN	2	0%	26-Mar-24	27-Mar-24	0	■ U/G TRENCH DRAIN																			
33	<b>FOUNDATIONS</b>		14		28-Mar-24	16-Apr-24	0	○ 16-Apr-24, FOUNDATIONS																			
34	260.FND	SURVEY GRIDS / SET BENCHMARK FOR FINISH FLOOR	1	0%	28-Mar-24	28-Mar-24	0	SURVEY GRIDS / SET BENCHMARK FOR FINISH FLOOR																			
35	261.FND	EXCAVATE FOUNDATIONS	3	0%	29-Mar-24	02-Apr-24	0	■ EXCAVATE FOUNDATIONS																			
36	262.FND	TEST BOTTOM OF FOOTING	1	0%	03-Apr-24	03-Apr-24	0	TEST BOTTOM OF FOOTING																			
37	263.FND	FORM FOUNDATIONS / COLUMN PADS	2	0%	04-Apr-24	05-Apr-24	0	■ FORM FOUNDATIONS / COLUMN PADS																			
38	264.FND	REINFORCEMENT / EMBEDS FOR STEEL FOUNDATIONS / COLUMN PADS	2	0%	08-Apr-24	09-Apr-24	0	■ REINFORCEMENT / EMBEDS FOR STEEL FOUNDATIONS / COLUMN PADS																			
39	265.FND	MEPF SLEEVES / STUBS IN FOUNDATIONS	2	0%	10-Apr-24	11-Apr-24	0	■ MEPF SLEEVES / STUBS IN FOUNDATIONS																			
40	266.FND	SET ANCHOR BOLT TEMPLATES	1	0%	12-Apr-24	12-Apr-24	0	SET ANCHOR BOLT TEMPLATES																			
41	267.FND	POUR FOUNDATIONS / DEPRESSED SLAB / COLUMN PADS	1	0%	15-Apr-24	15-Apr-24	0	POUR FOUNDATIONS / DEPRESSED SLAB / COLUMN PADS																			
42	268.FND	STRIP / CLEAN	1	0%	16-Apr-24	16-Apr-24	0	STRIP / CLEAN																			
43	<b>SOG</b>		9		17-Apr-24	29-Apr-24	0	○ 29-Apr-24, SOG																			
44	280.SOG	FORM SOG	2	0%	17-Apr-24	18-Apr-24	0	■ FORM SOG																			
45	281.SOG	4" CAPILLARY FILL	1	0%	19-Apr-24	19-Apr-24	0	4" CAPILLARY FILL																			
46	282.SOG	VAPOR BARRIER OVER 4" CAPILLARY FILL	2	0%	22-Apr-24	23-Apr-24	0	■ VAPOR BARRIER OVER 4" CAPILLARY FILL																			
47	283.SOG	REINFORCE SOG	2	0%	24-Apr-24	25-Apr-24	0	■ REINFORCE SOG																			
48	284.SOG	POUR / FINISH / CURE SOG	1	0%	26-Apr-24	26-Apr-24	0	POUR / FINISH / CURE SOG																			
49	285.SOG	STRIP SOG	1	0%	29-Apr-24	29-Apr-24	0	STRIP SOG																			
50	<b>STRUCTURE</b>		22		30-Apr-24	30-May-24	74	○ 30-May-24, STRUCTURE																			
51	300.STRC	MOBILIZE / SET UP CRANE	1	0%	30-Apr-24	30-Apr-24	0	MOBILIZE / SET UP CRANE																			

■ Actual Level of Effort    ○ summary  
■ Actual Work  
■ Remaining Work  
■ Critical Remaining Work  
◆ Milestone

**BASELINE  
ALL**

Page 2 of 9  
 Data Date: 13-Feb-24  
 Run Date: 26-Jan-24 / 14:17


#	Activity ID	Activity Name	Original Duration	% Complete	Start	Finish	Total Float	2024												2025							
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
52	301.STRC	ERECT STRUCTURAL STEEL	4	0%	01-May-24	06-May-24	0	■ ERECT STRUCTURAL STEEL																			
53	302.STRC	DECKING / WELDING	3	0%	07-May-24	09-May-24	0	■ DECKING / WELDING																			
54	303.STRC	PLUMB / LINE / WELD STRUCTURAL STEEL	4	0%	10-May-24	15-May-24	0	■ PLUMB / LINE / WELD STRUCTURAL STEEL																			
55	2ND FLOOR / CATWALK		14		10-May-24	30-May-24	74	○ 30-May-24, 2ND FLOOR / CATWALK																			
56	310.CTWLK	DECKING / WELDING	3	0%	10-May-24	14-May-24	74	■ DECKING / WELDING																			
57	311.CTWLK	PLACE CATWALK	1	0%	15-May-24	15-May-24	74	PLACE CATWALK																			
58	312.CTWLK	STEEL STAIRS	3	0%	16-May-24	20-May-24	74	■ STEEL STAIRS																			
59	313.CTWLK	LADDER	2	0%	21-May-24	22-May-24	74	LADDER																			
60	314.CTWLK	GUARDRAIL	5	0%	23-May-24	30-May-24	74	■ GUARDRAIL																			
61	ROOF (PBR ROOF)		31		16-May-24	28-Jun-24	53	○ 28-Jun-24, ROOF (PBR ROOF)																			
62	320.RF	FRAMING FOR STEEL GIRDERS	10	0%	16-May-24	30-May-24	7	■ FRAMING FOR STEEL GIRDERS																			
63	321.RF	ROOF METAL PANELS	5	0%	31-May-24	06-Jun-24	7	■ ROOF METAL PANELS																			
64	322.RF	ROOF PENETRATIONS MEPF	3	0%	07-Jun-24	11-Jun-24	53	■ ROOF PENETRATIONS MEPF																			
65	323.RF	MECHANICAL EQUIPMENT UNDERNEATH ROOF	5	0%	12-Jun-24	18-Jun-24	53	■ MECHANICAL EQUIPMENT UNDERNEATH ROOF																			
66	324.RF	ELECTRICAL EQUIPMENT FOR MECHANICAL	3	0%	19-Jun-24	21-Jun-24	53	■ ELECTRICAL EQUIPMENT FOR MECHANICAL																			
67	325.RF	PLUMBING EQUIPMENT FOR MECHANICAL	3	0%	24-Jun-24	26-Jun-24	53	■ PLUMBING EQUIPMENT FOR MECHANICAL																			
68	326.RF	ROOF INSULATION	2	0%	27-Jun-24	28-Jun-24	53	ROOF INSULATION																			
69	EXTERIOR		20		07-Jun-24	05-Jul-24	49	○ 05-Jul-24, EXTERIOR																			
70	NORTH (A3.01) - METAL WALL PANEL		7		07-Jun-24	17-Jun-24	7	○ 17-Jun-24, NORTH (A3.01) - METAL WALL PANEL																			
71	330.EXTN	EXTERIOR METAL PANELS - N	7	0%	07-Jun-24	17-Jun-24	7	■ EXTERIOR METAL PANELS - N																			
72	EAST (A3.01) - METAL WALL PANEL, ROLL UP GARAGE DOOR		11		18-Jun-24	02-Jul-24	51	○ 02-Jul-24, EAST (A3.01) - METAL WALL PANEL, ROLL UP GARAGE DOOR																			
73	340.EXTE	EXTERIOR METAL PANELS - E	3	0%	18-Jun-24	20-Jun-24	7	■ EXTERIOR METAL PANELS - E																			
74	341.EXTE	FRAMING FOR ROLL UP DOORS	5	0%	21-Jun-24	27-Jun-24	51	■ FRAMING FOR ROLL UP DOORS																			
75	342.EXTE	ROLL UP DOOR INSTALLATION	3	0%	28-Jun-24	02-Jul-24	51	■ ROLL UP DOOR INSTALLATION																			
76	SOUTH (A3.01) - METAL WALL PANEL		2		21-Jun-24	24-Jun-24	7	○ 24-Jun-24, SOUTH (A3.01) - METAL WALL PANEL																			
77	350.EXTS	EXTERIOR METAL PANELS - S	2	0%	21-Jun-24	24-Jun-24	7	■ EXTERIOR METAL PANELS - S																			
78	WEST (A3.01) - METAL WALL PANEL, DOOR AND FRAME		8		25-Jun-24	05-Jul-24	49	○ 05-Jul-24, WEST (A3.01) - METAL WALL PANEL, DOOR AND FRAME																			

-  Actual Level of Effort
-  Actual Work
-  Remaining Work
-  Critical Remaining Work
-  Milestone

○ summary

**BASELINE  
ALL**

#	Activity ID	Activity Name	Original Duration	% Complete	Start	Finish	Total Float	2024												2025							
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
79	360.EXTW	EXTERIOR METAL PANELS - W	5	0%	25-Jun-24	01-Jul-24	7																				
80	361.EXTW	FRAMING FOR DOORS	1	0%	02-Jul-24	02-Jul-24	49																				
81	362.EXTW	DOOR INSTALLATION	2	0%	03-Jul-24	05-Jul-24	49																				
82	INTERIOR BUILDOUT		85		16-May-24	16-Sep-24	0																				
83	SERVICE BAY (RM 101) / PARTS STORAGE (RM 102)		84		16-May-24	13-Sep-24	0																				
84	ROUGH IN		54		16-May-24	01-Aug-24	0																				
85	370.SRPRT	LAYOUT TOP TRACK & WALLS - RM 101/102	2	0%	16-May-24	17-May-24	0																				
86	371.SRPRT	PRIORITY WALLS / FRAMES - RM 101/102	3	0%	20-May-24	22-May-24	0																				
87	372.SRPRT	OH FIRE PROTECTION - RM 101/102	4	0%	23-May-24	29-May-24	0																				
88	373.SRPRT	OH PLUMBING - RM 101/102	4	0%	30-May-24	04-Jun-24	0																				
89	374.SRPRT	OH MECHANICAL - RM 101/102	7	0%	05-Jun-24	13-Jun-24	0																				
90	375.SRPRT	OH ELECTRICAL - RM 101/102	7	0%	14-Jun-24	24-Jun-24	0																				
91	376.SRPRT	OH FA / LV - RM 101/102	7	0%	25-Jun-24	03-Jul-24	0																				
92	377.SRPRT	DOOR FRAMES - RM 101/102	2	0%	05-Jul-24	08-Jul-24	0																				
93	378.SRPRT	ELECTRICAL/LV IN-WALL RI - RM 101/102	2	0%	09-Jul-24	10-Jul-24	0																				
94	379.SRPRT	PLUMBING IN-WALL RI - RM 101/102	2	0%	11-Jul-24	12-Jul-24	0																				
95	380.SRPRT	MECHANICAL / CONTROLS IN-WALL RI - RM 101/102	2	0%	15-Jul-24	16-Jul-24	0																				
96	381.SRPRT	IN-WALL INSPECTION (PRE-COVER) TO ALLOW INSULATION - RM 101/102	1	0%	17-Jul-24	17-Jul-24	0																				
97	382.SRPRT	PULL WIRE - RM 101/102	3	0%	18-Jul-24	22-Jul-24	0																				
98	383.SRPRT	DRYWALL - RM 101/102	4	0%	23-Jul-24	26-Jul-24	0																				
99	384.SRPRT	CLOSURE INSPECTION @ WALLS / SOFFITS - RM 101/102	1	0%	29-Jul-24	29-Jul-24	0																				
100	385.SRPRT	BALANCE DRYWALL - RM 101/102	3	0%	30-Jul-24	01-Aug-24	0																				
101	FINISHES		30		02-Aug-24	13-Sep-24	0																				
102	400.SRPRT	TAPE AND FINISH - RM 101/102	3	0%	02-Aug-24	06-Aug-24	0																				
103	401.SRPRT	PAINT - RM 101/102	2	0%	07-Aug-24	08-Aug-24	0																				
104	402.SRPRT	LIGHT FIXTURES - RM 101/102	3	0%	09-Aug-24	13-Aug-24	0																				
105	403.SRPRT	MEPF TRIM - RM 101/102	3	0%	14-Aug-24	16-Aug-24	0																				

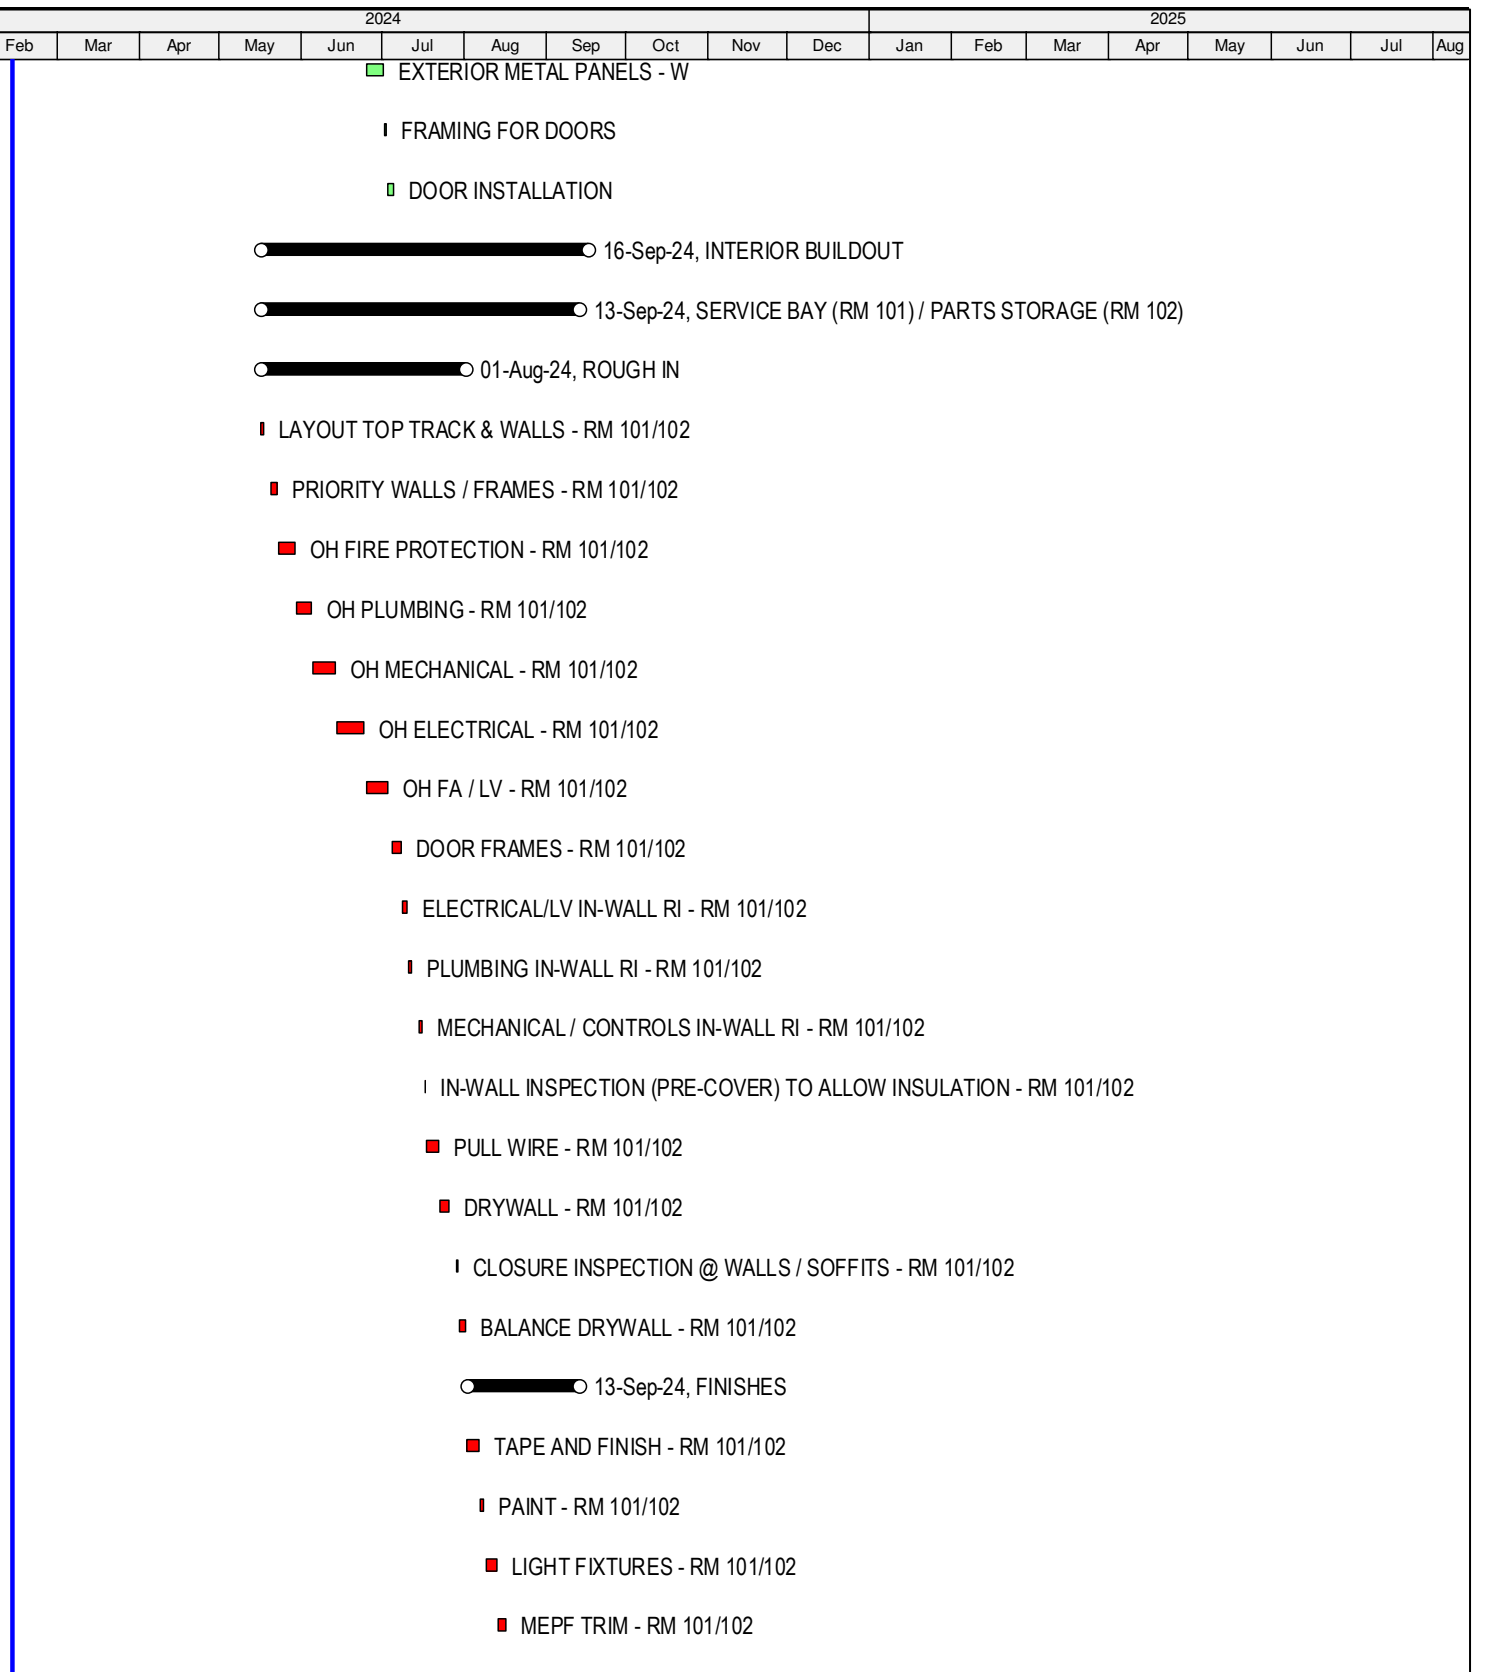

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- summary

BASELINE  
ALL

#	Activity ID	Activity Name	Original Duration	% Complete	Start	Finish	Total Float	2024												2025							
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
106	404.SRVPRTF	SEALED CONCRETE - RM 101/102	2	0%	19-Aug-24	20-Aug-24	0	■ SEALED CONCRETE - RM 101/102																			
107	405.SRVPRTF	CASEWORK - RM 101/102	3	0%	21-Aug-24	23-Aug-24	0	■ CASEWORK - RM 101/102																			
108	406.SRVPRTF	COUNTERTOPS - RM 101/102	2	0%	26-Aug-24	27-Aug-24	0	■ COUNTERTOPS - RM 101/102																			
109	407.SRVPRTF	SIGNAGE - RM 101/102	1	0%	28-Aug-24	28-Aug-24	0	SIGNAGE - RM 101/102																			
110	408.SRVPRTF	INSTALL ACCESS PANELS - RM 101/102	1	0%	29-Aug-24	29-Aug-24	0	INSTALL ACCESS PANELS - RM 101/102																			
111	409.SRVPRTF	DOORS & HARDWARE - RM 101/102	3	0%	30-Aug-24	04-Sep-24	0	■ DOORS & HARDWARE - RM 101/102																			
112	410.SRVPRTF	TIRE CLAMP - RM 101/102	1	0%	05-Sep-24	05-Sep-24	0	TIRE CLAMP - RM 101/102																			
113	411.SRVPRTF	BRAKE LATHE - RM 101/102	1	0%	06-Sep-24	06-Sep-24	0	BRAKE LATHE - RM 101/102																			
114	412.SRVPRTF	TABLE GRINDER - RM 101/102	1	0%	09-Sep-24	09-Sep-24	0	TABLE GRINDER - RM 101/102																			
115	413.SRVPRTF	DRILL PRESS - RM 101/102	1	0%	10-Sep-24	10-Sep-24	0	DRILL PRESS - RM 101/102																			
116	414.SRVPRTF	OIL FILTER CRUSHER - RM 101/102	1	0%	11-Sep-24	11-Sep-24	0	OIL FILTER CRUSHER - RM 101/102																			
117	415.SRVPRTF	MIG WELDER - RM 101/102	1	0%	12-Sep-24	12-Sep-24	0	MIG WELDER - RM 101/102																			
118	416.SRVPRTF	CHARGING STATION - RM 101/102	1	0%	13-Sep-24	13-Sep-24	0	CHARGING STATION - RM 101/102																			
119	OFFICE (RM 103)		81		16-May-24	10-Sep-24	3	○ 10-Sep-24, OFFICE (RM 103)																			
120	ROUGH IN		54		16-May-24	01-Aug-24	3	○ 01-Aug-24, ROUGH IN																			
121	430.OFRI	LAYOUT TOP TRACK & WALLS - RM 103	2	0%	16-May-24	17-May-24	3	■ LAYOUT TOP TRACK & WALLS - RM 103																			
122	431.OFRI	PRIORITY WALLS / FRAMES - RM 103	3	0%	20-May-24	22-May-24	3	■ PRIORITY WALLS / FRAMES - RM 103																			
123	432.OFRI	OH FIRE PROTECTION - RM 103	4	0%	23-May-24	29-May-24	3	■ OH FIRE PROTECTION - RM 103																			
124	433.OFRI	OH PLUMBING - RM 103	4	0%	30-May-24	04-Jun-24	3	■ OH PLUMBING - RM 103																			
125	434.OFRI	OH MECHANICAL - RM 103	7	0%	05-Jun-24	13-Jun-24	3	■ OH MECHANICAL - RM 103																			
126	435.OFRI	OH ELECTRICAL - RM 103	7	0%	14-Jun-24	24-Jun-24	3	■ OH ELECTRICAL - RM 103																			
127	436.OFRI	OH FA / LV - RM 103	7	0%	25-Jun-24	03-Jul-24	3	■ OH FA / LV - RM 103																			
128	437.OFRI	DOOR FRAMES - RM 103	2	0%	05-Jul-24	08-Jul-24	3	■ DOOR FRAMES - RM 103																			
129	438.OFRI	ELECTRICAL/LV IN-WALL RI - RM 103	2	0%	09-Jul-24	10-Jul-24	3	■ ELECTRICAL/LV IN-WALL RI - RM 103																			
130	439.OFRI	PLUMBING IN-WALL RI - RM 103	2	0%	11-Jul-24	12-Jul-24	3	■ PLUMBING IN-WALL RI - RM 103																			
131	440.OFRI	MECHANICAL / CONTROLS IN-WALL RI - RM 103	2	0%	15-Jul-24	16-Jul-24	3	■ MECHANICAL / CONTROLS IN-WALL RI - RM 103																			
132	441.OFRI	IN-WALL INSPECTION (PRE-COVER) TO ALLOW INSULATION - RM 103	1	0%	17-Jul-24	17-Jul-24	3	IN-WALL INSPECTION (PRE-COVER) TO ALLOW INSULATION - RM 103																			

Actual Level of Effort    summary
   
 Actual Work
   
 Remaining Work
   
 Critical Remaining Work
   
 Milestone

**BASELINE**  
**ALL**

Page 5 of 9  
 Data Date: 13-Feb-24  
 Run Date: 26-Jan-24 / 14:17

#	Activity ID	Activity Name	Original Duration	% Complete	Start	Finish	Total Float	2024												2025							
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
133	442.OFRI	PULL WIRE - RM 103	3	0%	18-Jul-24	22-Jul-24	3																				
134	443.OFRI	DRYWALL - RM 103	4	0%	23-Jul-24	26-Jul-24	3																				
135	444.OFRI	CLOSURE INSPECTION @ WALLS / SOFFITS - RM 103	1	0%	29-Jul-24	29-Jul-24	3																				
136	445.OFRI	BALANCE DRYWALL - RM 103	3	0%	30-Jul-24	01-Aug-24	3																				
137	<b>FINISHES</b>		<b>27</b>		<b>02-Aug-24</b>	<b>10-Sep-24</b>	<b>3</b>																				
138	460.OFF	TAPE AND FINISH - RM 103	3	0%	02-Aug-24	06-Aug-24	3																				
139	461.OFF	PAINT - RM 103	2	0%	07-Aug-24	08-Aug-24	3																				
140	462.OFF	SUSPENDED ACOUSTIC TILE - RM 103	5	0%	09-Aug-24	15-Aug-24	3																				
141	463.OFF	LIGHT FIXTURES - RM 103	3	0%	16-Aug-24	20-Aug-24	3																				
142	464.OFF	MEPF TRIM - RM 103	3	0%	21-Aug-24	23-Aug-24	3																				
143	465.OFF	SEALED CONCRETE - RM 103	2	0%	26-Aug-24	27-Aug-24	3																				
144	466.OFF	CASEWORK - RM 103	3	0%	28-Aug-24	30-Aug-24	3																				
145	467.OFF	COUNTERTOPS - RM 103	2	0%	03-Sep-24	04-Sep-24	3																				
146	468.OFF	SIGNAGE - RM 103	1	0%	05-Sep-24	05-Sep-24	3																				
147	469.OFF	DOORS & HARDWARE - RM 103	3	0%	06-Sep-24	10-Sep-24	3																				
148	<b>MECHANICAL ROOM (RM 104)</b>		<b>66</b>		<b>16-May-24</b>	<b>19-Aug-24</b>	<b>18</b>																				
149	<b>ROUGH IN</b>		<b>48</b>		<b>16-May-24</b>	<b>24-Jul-24</b>	<b>18</b>																				
150	480.MCH	LAYOUT TOP TRACK & WALLS - RM 104	2	0%	16-May-24	17-May-24	18																				
151	481.MCH	PRIORITY WALLS / FRAMES - RM 104	3	0%	20-May-24	22-May-24	18																				
152	482.MCH	OH FIRE PROTECTION - RM 104	4	0%	23-May-24	29-May-24	18																				
153	483.MCH	OH MECHANICAL - RM 104	4	0%	30-May-24	04-Jun-24	18																				
154	484.MCH	OH ELECTRICAL - RM 104	7	0%	05-Jun-24	13-Jun-24	18																				
155	485.MCH	OH FA / LV - RM 104	7	0%	14-Jun-24	24-Jun-24	18																				
156	486.MCH	SET HOLLOW METAL FRAMES - RM 104	2	0%	25-Jun-24	26-Jun-24	18																				
157	488.MCH	COUNTERTOP SUPPORTS - RM 104	2	0%	27-Jun-24	28-Jun-24	18																				
158	487.MCH	BACKING - RM 104	2	0%	01-Jul-24	02-Jul-24	18																				
159	489.MCH	ELECTRICAL/LV IN-WALL RI - RM 104	2	0%	03-Jul-24	05-Jul-24	18																				

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- summary

**BASELINE  
ALL**

#	Activity ID	Activity Name	Original Duration	% Complete	Start	Finish	Total Float	2024												2025							
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
160	490.MCH	PLUMBING IN-WALL RI - RM 104	2	0%	08-Jul-24	09-Jul-24	18																				
161	491.MCH	MECHANICAL / CONTROLS IN-WALL RI - RM 104	2	0%	10-Jul-24	11-Jul-24	18																				
162	492.MCH	IN-WALL INSPECTION (PRE-COVER) TO ALLOW INSULATION - RM 104	1	0%	12-Jul-24	12-Jul-24	18																				
163	493.MCH	ONE-SIDE DRYWALL - RM 104	4	0%	15-Jul-24	18-Jul-24	18																				
164	494.MCH	PULL WIRE - RM 104	3	0%	19-Jul-24	23-Jul-24	18																				
165	495.MCH	CLOSURE INSPECTION @ WALLS / SOFFITS - RM 104	1	0%	24-Jul-24	24-Jul-24	18																				
166	FINISHES		18		25-Jul-24	19-Aug-24	18																				
167	510.MCHF	BALANCE DRYWALL - RM 104	3	0%	25-Jul-24	29-Jul-24	18																				
168	511.MCHF	TAPE AND FINISH - RM 104	3	0%	30-Jul-24	01-Aug-24	18																				
169	512.MCHF	PAINT - RM 104	2	0%	02-Aug-24	05-Aug-24	18																				
170	513.MCHF	MEPF TRIM - RM 104	3	0%	06-Aug-24	08-Aug-24	18																				
171	514.MCHF	SEALED CONCRETE - RM 104	2	0%	09-Aug-24	12-Aug-24	18																				
172	515.MCHF	SIGNAGE - RM 104	1	0%	13-Aug-24	13-Aug-24	18																				
173	516.MCHF	INSTALL ACCESS PANELS - RM 104	1	0%	14-Aug-24	14-Aug-24	18																				
174	517.MCHF	DOORS & HARDWARE - RM 104	3	0%	15-Aug-24	19-Aug-24	18																				
175	BUS WASH		45		20-May-24	23-Jul-24	38																				
176	520.BUS	OVERHEAD MEP	15	0%	20-May-24	10-Jun-24	38																				
177	521.BUS	IN-WALL MEP	15	0%	11-Jun-24	01-Jul-24	38																				
178	522.BUS	BUSWASH EQUIPMENT	15	0%	02-Jul-24	23-Jul-24	38																				
179	PUNCHLIST		1		16-Sep-24	16-Sep-24	0																				
180	530.PNC	READY FOR PUNCHLIST	1	0%	16-Sep-24	16-Sep-24	0																				
181	UTILITIES		41		16-May-24	15-Jul-24	48																				
182	SANITARY SEWER		12		16-May-24	03-Jun-24	45																				
183	540.UTLSS	EXCAVATE TRENCH - SANITARY SEWER	3	0%	16-May-24	20-May-24	45																				
184	541.UTLSS	BEDDING - SANITARY SEWER	1	0%	21-May-24	21-May-24	45																				
185	542.UTLSS	PIPING - SANITARY SEWER	5	0%	22-May-24	29-May-24	45																				
186	543.UTLSS	TESTING - SANITARY SEWER	1	0%	30-May-24	30-May-24	45																				



■ Actual Level of Effort    ● summary  
■ Actual Work  
■ Remaining Work  
■ Critical Remaining Work  
◆ Milestone

**BASELINE  
ALL**

Page 7 of 9  
Data Date: 13-Feb-24  
Run Date: 26-Jan-24 / 14:17

#	Activity ID	Activity Name	Original Duration	% Complete	Start	Finish	Total Float	2024												2025															
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug									
187	544.UTLSS	BACKFILL - ONSITE SANITARY SEWER	2	0%	31-May-24	03-Jun-24	45																												
188	STORM DRAIN		12		04-Jun-24	19-Jun-24	45																												
189	560.UTLSD	EXCAVATE TRENCH - STORM DRAIN	3	0%	04-Jun-24	06-Jun-24	45																												
190	561.UTLSD	BEDDING - STORM DRAIN	1	0%	07-Jun-24	07-Jun-24	45																												
191	562.UTLSD	PIPING - STORM DRAIN	5	0%	10-Jun-24	14-Jun-24	45																												
192	563.UTLSD	TESTING - STORM DRAIN	1	0%	17-Jun-24	17-Jun-24	45																												
193	564.UTLSD	BACKFILL - STORM DRAIN	2	0%	18-Jun-24	19-Jun-24	45																												
194	ELECTRICAL		15		20-Jun-24	11-Jul-24	45																												
195	580.UTLEL	EXCAVATE ELECTRICAL	3	0%	20-Jun-24	24-Jun-24	45																												
196	581.UTLEL	PLACE VAULT / PULL BOXES - ELECTRICAL	1	0%	25-Jun-24	25-Jun-24	45																												
197	582.UTLEL	CONCRETE ENCASEMENT - ELECTRICAL	2	0%	26-Jun-24	27-Jun-24	45																												
198	583.UTLEL	BACKFILL - ELECTRICAL	2	0%	28-Jun-24	01-Jul-24	45																												
199	584.UTLEL	ELECTRICAL CONDUITS	3	0%	02-Jul-24	05-Jul-24	45																												
200	585.UTLEL	PULL WIRE	2	0%	08-Jul-24	09-Jul-24	45																												
201	586.UTLEL	TEST	1	0%	10-Jul-24	10-Jul-24	45																												
202	587.UTLEL	ENERGIZE	1	0%	11-Jul-24	11-Jul-24	45																												
203	GAS		9		02-Jul-24	15-Jul-24	48																												
204	600.UTLG	EXCAVATE TRENCH - GAS	3	0%	02-Jul-24	05-Jul-24	48																												
205	601.UTLG	BEDDING - GAS	1	0%	08-Jul-24	08-Jul-24	48																												
206	602.UTLG	GAS LINE - GAS	2	0%	09-Jul-24	10-Jul-24	48																												
207	603.UTLG	TESTING - GAS	1	0%	11-Jul-24	11-Jul-24	48																												
208	604.UTLG	BACKFILL - GAS	2	0%	12-Jul-24	15-Jul-24	48																												
209	SITEWORK PHASE 1		50		02-Jul-24	11-Sep-24	7																												
210	620.STE	METAL FENCE / GATES FOOTINGS - SITE PH1	15	0%	02-Jul-24	23-Jul-24	7																												
211	621.STE	CHAIN LINK FENCE / GATE FOOTINGS - SITE PH1	10	0%	24-Jul-24	06-Aug-24	7																												
212	622.STE	CURB AND GUTTER - SITE PH1	10	0%	07-Aug-24	20-Aug-24	7																												
213	623.STE	MANHOLE ADJUSTMENT - SITE PH1	3	0%	21-Aug-24	23-Aug-24	7																												






- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- summary

**BASELINE**  
**ALL**

Page 8 of 9  
Data Date: 13-Feb-24  
Run Date: 26-Jan-24 / 14:17



#	Activity ID	Activity Name	Original Duration	% Complete	Start	Finish	Total Float	2024												2025																				
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug														
214	624.STE	PAVING / PAVEMENT - SITE PH1	7	0%	26-Aug-24	04-Sep-24	7																																	
215	625.STE	STRIPE & SIGNAGE - SITE PH1	3	0%	05-Sep-24	09-Sep-24	7																																	
216	626.STE	CLEAN UP DEMOBE - SITE PH1	2	0%	10-Sep-24	11-Sep-24	7																																	
217	PUNCH LIST / COMMISSIONING / CLOSE OUT		20		12-Sep-24	09-Oct-24	0																																	
218	640.CX	AMG PUNCHLIST (EXTERIOR)	10	0%	12-Sep-24	25-Sep-24	7																																	
219	641.CX	AMG PUNCHLIST (INTERIOR)	5	0%	17-Sep-24	23-Sep-24	0																																	
220	642.CX	AMG COMPLETION LIST (INTERIOR)	1	0%	24-Sep-24	24-Sep-24	0																																	
221	643.CX	OWNER / AE PUNCHLIST	1	0%	25-Sep-24	25-Sep-24	0																																	
222	644.CX	OWNER / AE COMPLETION LIST	1	0%	26-Sep-24	26-Sep-24	0																																	
223	645.CX	START UP (INTERIOR)	1	0%	27-Sep-24	27-Sep-24	0																																	
224	646.CX	AIR BALANCE TESTING	1	0%	30-Sep-24	30-Sep-24	0																																	
225	647.CX	TESTING OF SYSTEM	2	0%	01-Oct-24	02-Oct-24	0																																	
226	648.CX	FINAL PUNCHLIST	2	0%	03-Oct-24	04-Oct-24	0																																	
227	649.CX	PROJECT CLOSE-OUT / O&M'S	2	0%	07-Oct-24	08-Oct-24	0																																	
228	650.CX	DEMOBILIZATION	1	0%	09-Oct-24	09-Oct-24	0																																	
229	651.CX	END OF PROJECT (6/20/24)	1	0%	09-Oct-24	09-Oct-24	0																																	

 Actual Level of Effort    ○ summary  
 Actual Work  
 Remaining Work  
 Critical Remaining Work  
 Milestone

**BASELINE**  
**ALL**

Page 9 of 9  
 Data Date: 13-Feb-24  
 Run Date: 26-Jan-24 / 14:17
